




NATIONAL MUSEUMS OF KENYA

WHERE HERITAGE LIVES ON

PROPOSED ABLUTION FACILITY AT THE INSTITUTE OF PRIMATE RESEARCH (IPR) AT KAREN

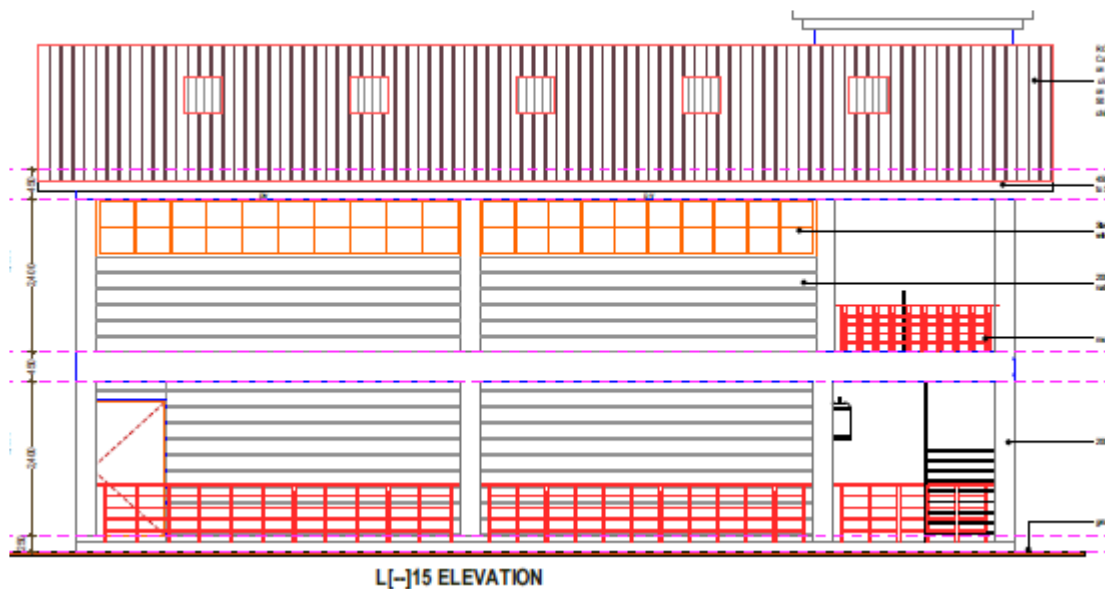

PENULTIMATE PAYMENT CERTIFICATE NO.02

Quantity Surveyors:

Integrity Quantity Surveyors
P.O. BOX 15521-00100,
Nairobi

Services Engineers:

Plancad Associates
P.O. BOX 67605 -00100
Nairobi

Architects:

Archscan Associates Limited
P.O. BOX 10958 -00100
Nairobi

Civil & Structural Engineers:

Strut Edge Solutions
P.O. BOX 2701-00100
Nairobi

18TH FEBRUARY, 2020

Client Award Letter



INSTITUTE OF PRIMATE RESEARCH

P.O. Box 24481 - 00502 Karen, Nairobi. Tel: (+254-20) 2606235 Fax: (+254-20) 2606231
URL: www.primateresearch.org | Email: directoripr@primateresearch.org



Our Ref: IPR/ADM/SUP/1.199

Date: **Monday, 27th May, 2019**

M/s Roji Construction Limited
P.O. BOX 50426-00200,
Nairobi

Attention: Silah Joel /0722 924 379

Email: rojicon@gmail.com / rojicon@yahoo.com

Dear Sir,

RE: Proposed Ablution Block For The Institute of Primate Research Institute (IPR), Karen

Contract Offer

Above project and captioned matter refers.

Following the submission and opening of Tenders on **Friday, 10th May, 2019** for the above project, and after requisite analysis, we are happy to make a Contract Offer to your Company at your quoted Tender Sum of **Kshs. 4,310,000.00** (*Shillings Four Million Three Hundred and Ten Thousands inclusive VAT*) and a completion time of **Twelve (12) Weeks** subject to there being no objection/appeal by the other Tenderers before the scheduled commencement date.

Kindly note that the Formal Contract Commencement date for the Contract shall be **Monday, 1st July, 2019** and you may use the period in between for Mobilization

In the meantime, you may liaise directly with the Project Managers, M/s Archscan Associates Limited and the other listed Consultants all copied herein to secure pre contract documents (architectural & services drawings, civil, electrical & plumbing bills of quantities) for your use and preparation for commencement

You may also start making arrangements for processing all the required contract documents to facilitate Contract Signing (*Performance Bond, CAR /WIBA Insurances, Works schedule. Cash flow proposal etc.*).

Finally, please note that this Offer letter is subject to Contract and it does not authorize you to incur cost until actual contract has been signed on or before the indicated commencement date

Yours Faithfully,
Director

Dr Hastings Ozwara

DIRECTOR: INSTITUTE OF PRIMATE RESEARCH



Circulation

**Project Architects/Project Managers,
P.O. BOX 10958-00100,
Nairobi**

Attention: Architect Francis Macharia (0722 376969)

**Project Civil & Structural Engineers,
Strut Edge Solutions
P.O. BOX 2701-00100
Nairobi**

Attention: Engineer Anthony (0720 407 188)


**Project Quantity Surveyors,
Integrity Quantity Surveyors
P.O. BOX 15521-00100,
Nairobi**

Attention: QS Peter (0722 670 570)

**Project Services Engineers,
Checkom Consultants
P.O. BOX 22635 -00100
Nairobi**

Attention: Electrical Engineer Steven (0722 608 023)

Attention: Plumbing Engineer Simon (0725 501 759)


DIRECTOR

Architect Forwarding Letter

Our Ref: **MP/38/Ablution Block/ Architect Penultimate Payment Certificate /02**Date: **18th February, 2019****The Director,
Institute of Primate Research,
The National Museums of Kenya,
P.O. BOX 24481-00502,
Nairobi****Attention:** Dr Hastings Ozwara,

Dear Sir,

RE: Proposed Ablution Block For The Institute of Primate Research (IPR) , on Plot L.R. NO. 23268 at Karen, Nairobi County**Architect Penultimate Payment Certificate No.02**

Further to Ablution Block Contract Award Letter dated 27th May, 2019 (**Reference IPR/ADM/SUP/1.199**) and Pursuant to Clause 34.0 of the Building Contract (*Agreement and Conditions of Contract for Building Works*), please find attached herewith Architect's **Penultimate Payment Certificate No. 02** for **Kshs 2,944,177.30** (*Shillings Two Million, Nine Hundred Forty Four Thousands, One Hundred Seventy Seven Thirty Cents Only*) Payable to **M/s Roji Construction Limited** for works done and valued up to date and as specifically itemized in the attached summary of the attached Quantity Surveyors Penultimate Valuation No. 02 (*dated Thursday 13th February, 2020 Reference IQS/Ablution Block/Penultimate Valuation /02*) and the associated cost build ups for your record.

Table 1: Penultimate Payment Certificate No.02

	Item	Amount/Kshs	Notes
1	Preliminaries	0.00	See attached Quantity Surveyors Penultimate Valuation No. 02 dated Thursday 13 th February, 2020 (Reference IQS/Ablution Block/Interim Valuation /01)
2	Main Building	4,009,985.00	
3	Materials on Site	0.00	
4	Electrical Installations	262,850.00	See attached Electrical Engineers Penultimate Valuation No.02 dated 18.02.2020
5	Mechanical Installations	991,533.20	See attached Mechanical Engineers Penultimate Valuation No.02 dated 18.02.2020
6	Gross Penultimate Valuation No.02	5,264,368.20	
7	Less 5 % Retention	263,218.41	Payable after Six (6) Months Liability Period on
8	Amount Due	5,001,149.79	Penultimate Valuation No.02
9	Less Previous Payment Certificate No.01	2,056,972.50	
10	Amount Due Now	2,944,177.30	Certificate No.02 dated 18.02.2020 (Serial No.1020504)
11	Less 3 % With Holding Tax	76,142.50	PIN NO. P 051159467 N
12	Amount Payable to Contractor in Penultimate Certificate No.02	2,868,034.80	

Shillings Two Million Eight Hundred Sixty Eight Thousands, Thirty Four and Eighty Cents Only


Table 2: Final Account Variations Schedule

	Contract Item	Amount	Final	Variance	Notes
1	Sub Structure	715,150.00	995,275.00	280,125.00	<i>Increment due to First Floor Slab & Staircase Extensions</i>
2	Reinforced Concrete Superstructure	419,725.00	967,800.00	548,075.00	<i>Increment due to First Floor Slab & Staircase Extensions</i>
3	Walling	323,400.00	427,170.00	103,770.00	<i>Increment due to parapet walling on First Floor</i>
4	Roof	268,700.00	175,950.00	-92,750.00	<i>False roof to protect the First Floor Walling</i>
5	Finishes	517,250.00	954,240.00	436,990.00	<i>Increment due to Gypsum ceiling</i>
6	Windows	38,300.00	74,100.00	35,800.00	<i>Increment owing to bigger window openings</i>
7	Doors	214,360.00	259,580.00	45,220.00	<i>Increment owing to more door openings</i>
8	Plumbing & Drainage Installations	1,437,751.00	994,397.20	443,353.80	
9	Electrical Installations	375,364.00	262,850.00	112,514.00	
10	Vanity Tops	0.00	93,050.00	93,050.00	<i>New Item</i>
11	External Works (Manholes)	0.00	62,820.00	62,820.00	<i>Additional manholes</i>
	Total	4,310,000.00	5,267,232.20	957,232.20	

As can be seen from Table 2 above, there has been a cost increment of **Kshs 957,232.20** owing to inclusion and protection of the First Floor Reinforced Concrete Slab and associated Staircase (See attached Minutes No. 04/10, 04/11, 04/12, 04/14, 04/2020 , 05/11, 05/12, & 05/15, 05/28, 05/29, 05/30 & 05/31 Minutes Dated 3.10.2019 & 25.10.2019 (*References MP/38/Ablution Block/Site Meeting Minutes/04 & MP/38/Ablution Block/Site Meeting Minutes/05*) to serve the future Archive as requested by the Client

By Copy of this letter and pursuant Clause 34.0 and specifically sub Clause 34.23 of the Agreement and Conditions of Contract for Building Works, the Contractor, is requested to note that the Consultants/Client reserves the right to adjust the amount certified herein from any subsequent payments should the works be confirmed not to have been undertaken to the required contract standards and specifications or in absence of approval of material tests by the Structural Engineers (concrete, stones, aggregates etc).

Yours Faithfully



Francis Macharia
ARCHSCAN ASSOCIATES LIMITED

Circulation

**Project Quantity Surveyors,
Integrity Quantity Surveyors
P.O. BOX 15521-00100,
Nairobi**

Attention: QS Peter (0722 670 570)

**M/s Roji Construction Limited
P.O. BOX 50426-00200,
Nairobi**

Attention: Silah Joel /0722 924 379

Email: rojicon@gmail.com/ rojicon@yahoo.com



Serial No. **1020504**

INTERIM CERTIFICATE

Issue Date 18TH FEBRUARY, 2020
Certificate No. PENULTIMATE, No. 02
Contract Date 8-07-2019
Contract Sum KES 4,310,000/00

Job no MP/38/ABLUTION Block/2019
Job name ABLUTION BLOCK AT IPR, KAREN
Employer's name INSTITUTE OF PRIMATE RESEARCH (IPR) - KAREN
Address P.O. Box 24481-00502, NRB
Contractor's name ROJI CONSTRUCTION LTD
Address P.O. Box 50426-00200 NRB

I/we hereby certify that the sum of shillings TWO
MILLION, NINE HUNDRED FORTY
FOUR THOUSANDS, ONE HUNDRED
SEVENTY SEVEN THIRTY CENT
ONLY
KES 2,944,177/30

Present Instalment KES 2,944,177/30
Previous Instalment KES 2,056,972/50
Total Certified KES 5,001,149/80
Retention KES 263,218/40

is due to the contractor from the employer under terms of the contract on account of work carried out and/or materials supplied.

FRANCIS MACHARIA
NAME OF ARCHITECT / FIRM



A848

BORAQS
Registration No.

1807

AAK
Membership No.

CONTRACTOR'S RECEIPT

Received from _____
The sum of KES _____
In payment of cert. no _____ Date _____
The sum of KES _____

Serial No **1020504**

Date _____

STAMP

Quantity Surveyors Forwarding Letter



INTEGRITY QUANTITY SURVEYORS

Registered Quantity Surveyors, Property Valuations & Project Management

P.O. BOX 15521-00100, Tel 0722 670570 Nairobi Email: peter.ndung@yahoo.com

Our Ref: IQS/Ablution Block /Penultimate Valuation /02

Date: 13th February, 2020

**Archscan Associates Limited,
P.O. BOX 10958 -00100
NAIROBI**

Dear Sirs,

RE: Proposed Ablution Block For The Institute of Primate Research (IPR) , on Plot L.R. NO. 23268 at Karen, Nairobi County

Penultimate Valuation Statement No. 02


Please see attached summary of Penultimate Valuation No. 02 based on site re-measurements and attached Bills of Quantities tender rates following our site visit on Thursday, 13th February, 2020. We recommend that the below indicated amount of **Kshs 2,946,898.10** (*Shillings Two Million, Nine Hundred Forty Six Thousands, Eight Hundred Ninety Eight and Ten Cents Only*) be paid to **M/s Roji Construction Limited**

Table 1: Summary Penultimate Valuation Statement No. 02

	Item	Amount/Kshs	Notes
1	Preliminaries	0.00	See attached Quantity Surveyors Interim Valuation No. 01 dated Friday 30 th August, 2019 (Reference IQS/Ablution Block/Interim Valuation /01)
2	Main Building	4,009,985.00	
3	Materials on Site	0.00	
4	Electrical Installations	262,850.00	See attached Electrical Engineers Penultimate Valuation No.02 dated 18.02.2020
5	Mechanical Installations	991,533.20	See attached Mechanical Engineers Penultimate Valuation No.02 dated 18.02.2020
6	Gross Penultimate Valuation No.02	5,264,368.20	
7	Less 5 % retention	263,218.41	
8	Amount Due	5,001,149.79	Interim Valuation No.02
9	Less Previous Payment Certificate No.01	2,056,972.50	
10	Amount Payable to Contractor in Penultimate Valuation No.02	2,944,177.30	Certificate No.02 dated 18.02.2020 (Serial No.1020504)

Shillings Two Million, Nine Hundred Fourty Four Thousands, One Hundred Seventy Seven and Thirty Cents Only

Yours Faithfully


QS Peter Ndungu
For: Integrity Quantity Surveyors

Civil Works Site Re-Measurements Bills of Quantities

INTEGRITY QUANTITY SURVEYORS

QUANTITY SURVEYORS AND BUILDING ECONOMISTS

P.O. BOX 15521 – 00100 NAIROBI TEL 0722 670570

Date : 13th February 2020

**PROPOSED ABLUTION BLOCK AT THE TRAINING AND RESEARCH
CENTRE AT THE INSTITUTE OF PRIMATE RESEARCH FOR THE
NATIONAL MUSEUMS OF KENYA – KAREN**

We have visited the site and valued the work done and materials on site and would recommend that a Second Interim Certificate (Penultimate Certificate) in the amount of Ksh. 2,944,177.30 be issued to the Main Contractor Messrs Roji Construction Company Ltd. in accordance with the details below.

<u>SUMMARY OF VALUATION NO. 2 (PENULTIMATE VALUATION)</u>			
1	PRELIMINARIES		—
2	MAIN BUILDING		4,009,985.00
3	ELECTRICAL INSTALLATIONS		262,850.00
4	MECHANICAL INSTALLATIONS		991,533.20
GROSS VALUATION			5,264,368.20
Less 5 % retention (Practical Completion Achieved)			263,218.41
Amount due			5,001,149.79
<u>Less Previous payments</u>			
Valuation No. 1		2,056,972.50	2,056,972.50
Amount now due to Contractor in Penultimate Valuation No. 2			2,944,177.29

Issuance of a certificate of the amount of this valuation is subject to the Architect's satisfaction that work has been carried out in accordance with the drawings and specifications.

ABLUTION BLOCK

ITEM	DESCRIPTION	Bq Qty	Done	UNIT	RATE	BQ AMOUNT	VALUATION
	<u>SUBSTRUCTURES (PROVISIONAL) :-</u>						
A.	Site clearance to remove grass, shrubs, bushes and small trees	127	127	SM	25.00	3,175.00	3,175.00
B	Mass excavation to remove black cotton soil average 1.0 M deep	114	83	CM	300.00	34,200.00	24,900.00
C	Excavate trenches for strip foundations not exceeding 1.50 M deep from reduced level.	8	31	CM	250.00	2,000.00	7,750.00
D	Ditto for column bases ditto	3	16	CM	250.00	750.00	4,000.00
E	Load cart away or spread extra excavation material on site	98	93	CM	250.00	24,500.00	23,250.00
F	Return in, fill and ram well selected excavation materials	27	37	CM	150.00	4,050.00	5,550.00
G	Extra over excavation for rock excavation	2	0	CM	1,500.00	3,000.00	-
	<u>Filling</u>						
H	Selected hardcore filling under ground slab	74	55	CM	1,500.00	111,000.00	82,500.00
I	50 mm thick murram or quarry dust blinding to hardcore	82	92	SM	150.00	12,300.00	13,800.00
J	500 gauge damp proof membrane	82	92	SM	150.00	12,300.00	13,800.00
K	Chemical anti-termite treatment	82	92	SM	200.00	16,400.00	18,400.00
	<u>Plain concrete (1:4:8) as described in :-</u>						
L	50 mm thick under strip foundations	33	34	SM	400.00	13,200.00	13,600.00
M	50 mm thick under column bases	8	17	SM	400.00	3,200.00	6,800.00
	<u>Vibrated Reinforced Concrete class 20 in :-</u>						
A	Strip foundations	7	7	CM	13,500.00	94,500.00	94,500.00
B	Column bases and columns	3	6	CM	13,500.00	40,500.00	81,000.00
C	150 mm floor slab	82	92	SM	2,025.00	166,050.00	186,300.00
	<u>High Tensile Reinforcement Bars to B. S. 4461</u>						
D	Assorted reinforcement bars estimated at 50 Kg/CM	500	561	KG	150.00	75,000.00	84,150.00
	<u>Mesh fabric reinforcement</u>						
E	B. R. C. A 142 mesh reinforcement to Engineers specification	82	92	SM	450.00	36,900.00	41,400.00
	<u>Sawn formwork as described to :-</u>						
F	Sides of strip foundations	22	23	SM	500.00	11,000.00	11,500.00
G	Sides of column bases	10	17	SM	500.00	5,000.00	8,500.00
H	Sides of columns	7	10	SM	500.00	3,500.00	5,000.00
I	Edges of slab 75 mm - 150 mm high	41	42	LM	150.00	6,150.00	6,300.00
	<u>Natural stone walling bedded and jointed in cement and sand 1:3 mortar</u>						
A	200 mm thick	59	68	SM	1,800.00	106,200.00	122,400.00
	<u>Cement and sand 1:4 screed, wood floated</u>						
B	15 mm thick to plinth	20	20	SM	350.00	7,000.00	7,000.00
	<u>Prepare surface and apply two coats black bituminous paint on plinth surfaces</u>						
C	Plinth surface	20	20	SM	300.00	6,000.00	6,000.00
	<u>Items</u>						
D	Allow for keeping excavations clear of all water			ITEM		10,000.00	10,000.00
E	Allow for plunking and strutting			ITEM		10,000.00	10,000.00
	<u>Paving Slabs</u>						
F	600 x 600 x 50 mm thick pre-cast concrete paving slabs	32	62	SM	1,150.00	36,800.00	71,300.00
	<u>Abortive Works</u>						
*	Reinforcement in 3 No. column bases	0	60	KG	150.00	-	9,000.00
*	200 mm quarry stone foundation walling at the front	0	13	SM	1,800.00	-	23,400.00
	Total for Substructure carried to Summary					854,675.00	995,275.00

ITEM	DESCRIPTION	Bq Qty	Done	UNIT	RATE	BQ AMOUNT	VALUATION
	<u>ELEMENT NO. 2</u>						
	<u>R. C. SUPERSTRUCTURE :-</u>						
	<u>Reinforced Concrete class 20 as described to :-</u>						
A	Beams	4	7	CM	13,500.00	54,000.00	94,500.00
B	Columns	1	3	CM	13,500.00	13,500.00	40,500.00
C	Staircase	2	2	CM	13,500.00	27,000.00	27,000.00
D	150 mm thick suspended slab	66	74	SM	2,025.00	133,650.00	149,850.00
*	150 mm thick suspended slab overhang		8	SM	2,025.00	-	16,200.00
E	175 mm thick landing	9	10	SM	2,365.00	21,285.00	23,650.00
	<u>High Tensile Reinforcement Bars to B. S. 4461</u>						
G	Assorted reinforcement bars estimated at 100 Kg/CM	1,848	3,251	KG	150.00	277,200.00	487,650.00
	<u>Sawn Formwork as described to :-</u>						
H	Sides and soffits of beams	55	87	SM	500.00	27,500.00	43,500.00
I	Sides of columns	19	46	SM	500.00	9,500.00	23,000.00
J	Soffit of suspended slab	66	82	SM	500.00	33,000.00	41,000.00
K	Soffit of suspended landings	9	10	SM	500.00	4,500.00	5,000.00
	<u>Sawn Formwork Contd:-</u>						
A	Sloping soffit of staircase	7	7	SM	500.00	3,500.00	3,500.00
B	Edges of suspended slab 75 - 150 mm girth	35	40	LM	150.00	5,250.00	6,000.00
C	Edges of suspended landings 75 - 150 mm girth	12	13	LM	150.00	1,800.00	1,950.00
D	Edges of risers 75 - 150 mm girth	26	24	LM	150.00	3,900.00	3,600.00
E	Edges of staircase string 300 mm extreme girth cut to profile of risers and treads	6	6	LM	150.00	900.00	900.00
	Total for RC Superstructure carried to Summary					616,485.00	967,800.00
	<u>ELEMENT NO. 3</u>						
	<u>WALLING</u>						
	<u>External walling</u>						
	<u>Machine cut 'Thika' stone or other equal and approved walling :-</u>						
A	200 mm thick external wall	78	72	SM	1,800.00	140,400.00	129,600.00
*	200 mm thick parapet wall	0	62	SM	1,800.00	-	111,600.00
*	200 mm thick bud wall around paving slabs	0	11	SM	1,800.00	-	19,800.00
*	400 x 150 mm thick mass concrete haunching	0	26	LM	720.00	-	18,720.00
	<u>Internal walling</u>						
	<u>Machine cut 'Thika' stone or other equal and approved walling :-</u>						
C	200 mm thick	51	48	SM	1,800.00	91,800.00	86,400.00
D	150 mm thick	30	30	SM	1,800.00	54,000.00	54,000.00
	<u>Approved damp proof course laid to breaking joints</u>						
F	200 mm wide	36	36	LM	150.00	5,400.00	5,400.00
G	150 mm wide	11	11	LM	150.00	1,650.00	1,650.00
	Total for Walling carried to Summary					293,250.00	427,170.00

ITEM	DESCRIPTION	Bq Qty	Done	UNIT	RATE	BQ AMOUNT	VALUATION
<u>ELEMENT NO. 4</u>							
<u>ROOF</u>							
<u>32 gauge corrugated roofing sheets in:-</u>							
A	Sloping roof		111	SM	500.00	-	55,500.00
<u>Sawn Cypress roofing Timber</u>							
B	100 x 50 mm rafters		73	LM	450.00	-	32,850.00
C	75 x 50 mm struts/ties		34	LM	375.00	-	12,750.00
D	100 x 50 mm tie beams		63	LM	450.00	-	28,350.00
E	100 x 50 mm wall plate		15	LM	450.00	-	6,750.00
F	75 x 50 mm purlins		106	LM	375.00	-	39,750.00
Total for Walling carried to Summary						-	175,950.00
<u>ELEMENT NO. 5</u>							
<u>FINISHES</u>							
<u>Walls Finishes</u>							
A.	15 mm thick cement : sand (1:4) plaster to external surfaces	47	169	SM	350.00	16,450.00	59,150.00
*	15 mm thick cement : sand (1:4) plaster to bud walls		16	SM	350.00	-	5,600.00
B	Lime plaster to internal masonry or concrete surfaces	128	79	SM	350.00	44,800.00	27,650.00
C	15 mm plaster backing to receive wall tiles	125	159	SM	350.00	43,750.00	55,650.00
<u>External Painting</u>							
<u>Prepare surface and apply three coats "Duracoat" pure acrylic outdoor protector as per manufacturer's instructions:-</u>							
D	External wall and concrete surfaces	47	169	SM	300.00	14,100.00	50,700.00
<u>Key Pointing</u>							
E	10 mm half round neat horizontal joints in external walls	66	42	SM	300.00	19,800.00	12,600.00
F	6 mm thick coloured ceramic wall tiles as supplied by "Saj Ceramics" or other equal and approved.	125	159	SM	1,600.00	200,000.00	254,400.00
G	Approved quality corner strips	69	125	LM	250.00	17,250.00	31,250.00
<u>Internal Painting</u>							
<u>Prepare and apply three coats first quality silk vinyl matt paint to :-</u>							
H	Internal masonry or concrete surfaces	128	79	SM	300.00	38,400.00	23,700.00
<u>Floors</u>							
<u>Cement : sand (1:4) in :-</u>							
A	40 mm thick cement screed paving steel trowelled	82	83	SM	400.00	32,800.00	33,200.00
<u>Ceramic floor tiles</u>							
B	10 mm thick coloured ceramic floor tiles as supplied by "Saj Ceramics" or other equal and approved.	82	83	SM	1,600.00	131,200.00	132,800.00
<u>Skirtings</u>							
C	100 mm ceramic tile skirting	25	46	LM	400.00	10,000.00	18,400.00
<u>Ceiling finishes</u>							
<u>Lime plaster as described to:-</u>							
D	Suspended slab	66	74	SM	400.00	26,400.00	29,600.00
<u>Prepare and apply three coats first quality silk vinyl matt paint to :-</u>							
E	Plastered ceiling	66	74	SM	300.00	19,800.00	22,200.00
<u>Gypsum bulkhead</u>							
*	9 mm thick gypsum bulkhead including lightweight suspension and skimming		19	SM	3,100.00	-	58,900.00
*	100 mm gypsum cornice		17	LM	800.00	-	13,600.00
<u>Prepare and apply three coats first quality brilliant white matt paint to :-</u>							

ITEM	DESCRIPTION	Bq Qty	Done	UNIT	RATE	BQ AMOUNT	VALUATION
*	Gypsum ceiling		19	SM	300.00	-	5,700.00
*	Gypsm cornice 0 - 100 mm girth		17	LM	30.00	-	510.00
	<u>Staircase finishes</u>						
	<u>Cement and sand (1:3) screed in:-</u>						
A	20 mm thick paving in landings	9	6	SM	350.00	3,150.00	2,100.00
B	20 mm thick paving in treads; 250 mm wide	25	20	LM	90.00	2,250.00	1,800.00
C	15 mm thick paving in risers; 150 mm high	26	21	LM	60.00	1,560.00	1,260.00
	<u>Lime plaster as described to:-</u>						
D	Soffit of suspended landings	9	6	SM	350.00	3,150.00	2,100.00
E	Sloping soffit of staircase	7	7	SM	350.00	2,450.00	2,450.00
F	Edges of landings 75 mm - 150 mm girth	12	6	LM	60.00	720.00	360.00
G	Staircase string 200 - 300 mm girth	6	4	LM	110.00	660.00	440.00
	<u>Prepare and apply three coats first quality silk vinyl matt paint to :-</u>						
H	Soffit of suspended landings	9	6	SM	300.00	2,700.00	1,800.00
I	Sloping soffit of staircase	7	7	SM	300.00	2,100.00	2,100.00
J	Edges of landings 100 mm - 200 mm girth	12	6	LM	60.00	720.00	360.00
K	Staircase string 200 - 300 mm girth	6	4	LM	90.00	540.00	360.00
	<u>10 mm thick Ceramic floor tiles as supplied by "Tile & Carpet" or other equal and approved laid with mortar.</u>						
A	Landings	9		SM	1,600.00	14,400.00	-
B	Treads; 250 mm wide	25		LM	500.00	12,500.00	-
C	Risers; 150 mm high	26		LM	500.00	13,000.00	-
D	Skirtings; 100 mm high	12		LM	400.00	4,800.00	-
E	Approved quality edge strips	26		LM	250.00	6,500.00	-
	<u>Balustrading and railing</u>						
F	900 mm high mild steel staircase railing comprising of 65 mm diameter mild steel handrail, 50 x 50 x 4 mm thick Rectangular Hollow Section main balusters at 600 mm centres, 25 mm diameter mild steel in-fill balusters at 150 mm centres all to Architect's details. All steelwork to be primed with red oxide primer before fixing.	8	9	LM	5,500.00	44,000.00	49,500.00
G	Ditto in balconies ditto	15	9	LM	5,500.00	82,500.00	49,500.00
	<u>Touch up primer, prepare surface and apply one undercoat and two finishing coats of gloss oil paint to :-</u>						
H	Metal surfaces internally and externally	41	15	SM	300.00	12,300.00	4,500.00
	Total for Finishes carried to Summary					824,750.00	954,240.00
	<u>ELEMENT NO. 6</u>						
	<u>WINDOWS</u>						
	<u>Window Cill</u>						
A	250 x 75 mm thick prec-cast concrete window cill jointed and pointed in cement : sand (1:3) mortar	17		LM	500.00	8,500.00	-
	<u>Steel casement windows</u>						
	<u>Standard steel casement windows</u>						
B.	Window size 5300 x 900 mm high	1		NO	26,235.00	26,235.00	-
C	Window size 5850 x 900 mm high	1		NO	28,950.00	28,950.00	-
D	Window size 2400 x 900 mm high	2		NO	11,880.00	23,760.00	-
*	Window size 900 x 1800 mm high		2	NO	8,910.00	-	17,820.00
*	Window size 600 x 1000 mm high		1	NO	3,300.00	-	3,300.00
*	Window size 4000 x 600 mm high		1	NO	13,200.00	-	13,200.00
*	Window size 1800 x 600 mm high		1	NO	5,940.00	-	5,940.00

ITEM	DESCRIPTION	Bq Qty	Done	UNIT	RATE	BQ AMOUNT	VALUATION
*	Window size 2200 x 600 mm high		1	NO	7,260.00	-	7,260.00
*	Window size 1200 x 1300 mm high		1	NO	8,580.00	-	8,580.00
	<u>Glazing :-</u>						
	<u>4 mm thick obscure sheet glass fixed to metal with putty:-</u>						
F	Panes 0.1 - 0.5 square metres	14	10	SM	1,200.00	16,800.00	12,000.00
	<u>Touch up primer, prepare surface and apply one undercoat and two finishing coats of gloss oil paint to :-</u>						
A	Metal surfaces internally	14	10	SM	300.00	4,200.00	3,000.00
B	Metal surfaces externally	14	10	SM	300.00	4,200.00	3,000.00
	Total for Windows carried to Summary					112,645.00	74,100.00
	<u>ELEMENT NO. 7</u>						
	<u>DOORS (All to Architects details)</u>						
	<u>Steel casement door</u>						
	<u>Purpose made mild steel door divided into small panels glazed in 6 mm thick clear sheet glass. The door shall have 40 x 25 x 3 mm mild steel RHS main frame all round and all the carcass frames shall be 25 x 25 x 3 mm RHS. The door shall have purpose made heavy duty mild steel hinges and shall also be fitted with a padlock hasp for locking. All the steelwork shall be shop primed with one coat red oxide primer before erection.</u>						
A	Single door overall size 900 x 2400 mm high	2	2	NO	21,600.00	43,200.00	43,200.00
*	Single door overall size 1150 x 2500 mm high		1	NO	28,000.00	-	28,000.00
*	Single door overall size 800 x 2200 mm high		1	NO	17,600.00	-	17,600.00
	<u>Timber Doors</u>						
	<u>45 mm solid cored flush door faced both sides with plywood veneer and hardwood lipped all round</u>						
C	Door size 800 x 2400 mm with 300 x 800 mm fanlight	7	7	NO	5,500.00	38,500.00	38,500.00
D	Door size 1200 x 2400 mm with 300 x 1200 mm fanlight	1		NO	9,000.00	9,000.00	-
	<u>Wrot Mahogany: selected and kept clean :-</u>						
E	100 x 50 mm frame with labours	53	34	LM	1,500.00	79,500.00	51,000.00
F	50 x 25 mm architrave with two labours	46	34	LM	100.00	4,600.00	3,400.00
G	20 mm quarter-round beadings	46	34	LM	75.00	3,450.00	2,550.00
	<u>Supply and fix the following approved quality ironmongery to timber with matching screws :-</u>						
A	100 mm mild steel heavy duty butt hinges	16	10.5	PR	400.00	6,400.00	4,200.00
B	Aluminium mortice bathroom lock 'Union' 680/66/94 lock with Martin furniture, matching screws and a set of 3 keys	8	7	NO	3,500.00	28,000.00	24,500.00
C	Approved quality metal door lock	2	4	NO	7,500.00	15,000.00	30,000.00
	<u>Prepare and apply one coat aluminium wood primer to back of frame before fixing to :-</u>						
D	Surface 100 - 200 mm	53	34	LM	25.00	1,325.00	850.00
	<u>Touch up primer prepare surface and apply three coats gloss oil paint on metal surfaces as described</u>						
E	General metal surfaces	9	17	SM	300.00	2,700.00	5,100.00
	<u>Touch up primer prepare surface and apply three coats gloss oil paint on timber surfaces as described</u>						
F	General timber surfaces	33	22	SM	300.00	9,900.00	6,600.00
G	Timber surface 100 - 200 mm girth	53	34	LM	120.00	6,360.00	4,080.00
	<u>Glazing</u>						
	<u>5 mm thick clear sheet glass fixed to timber with glazing beads:-</u>						
H	Panes 0.1 - 0.5 square metres	2		SM	1,400.00	2,800.00	-
	Total for Doors carried to Summary					250,735.00	259,580.00

ITEM	DESCRIPTION	Bq Qty	Done	UNIT	RATE	BQ AMOUNT	VALUATION
	JOINERY FITTINGS						
	<u>Vanity Tops</u>						
A	100 mm thick concrete worktop		3	SM	1,350.00		4,050.00
B	BRC A142 mesh fabric reinforcement		3	SM	450.00		1,350.00
C	Steel reinforcement		30	KG	150.00		4,500.00
D	Formwork to soffits of worktop		3	SM	550.00		1,650.00
E	Formwork to edges of worktop 75 - 150 mm		6	LM	350.00		2,100.00
F	32 mm thick screed to worktop		3	SM	400.00		1,200.00
G	25 mm thick granite worktop		3	SM	15,500.00		46,500.00
H	100 mm high granite fascia		6	LM	1,250.00		7,500.00
I	Extra over granite for cutting hole for wash hand basin		6	NO	3,000.00		18,000.00
J	100 mm thick support wall		1	SM	1,800.00		1,800.00
K	Plaster to stone walling		2	SM	350.00		700.00
L	Ceramic tiles on stone walling		2	SM	1,600.00		3,200.00
M	Corner strips on ceramic tiles		2	LM	250.00		500.00
	Total for Vanity Tops carried to Summary					-	93,050.00
	EXTERNAL WORKS						
	<u>Manholes</u>						
A	600 x 450 x 1000 mm deep (internal dimensions) manholes		4	NO	10,000.00	-	40,000.00
B	150 mm PVC drain pipe		14	LM	550.00	-	7,700.00
C	100 mm PVC drain pipe		36	LM	350.00	-	12,600.00
D	Excavation for 150 mm drain pipe including backfilling		14	LM	180.00	-	2,520.00
	Total for External Works carried to Summary					-	62,820.00
	<u>SUMMARY OF GROUND FLOOR</u>					BQ AMOUNT	VALUATION
1	Substructure					854,675.00	995,275.00
2	Reinforced Concrete Superstructure					616,485.00	967,800.00
3	Walling					293,250.00	427,170.00
4	Temporary Roof					-	175,950.00
5	Finishes					824,750.00	954,240.00
6	Windows					112,645.00	74,100.00
7	Doors					250,735.00	259,580.00
8	Vanity Tops						93,050.00
9	External Works (Manholes)						62,820.00
	Total for Ablution Block carried to Summary of Valuation					2,952,540.00	4,009,985.00
