




NATIONAL MUSEUMS OF KENYA

WHERE HERITAGE LIVES ON

PROPOSED TRAINING AND RESOURCE CENTRE AT THE INSTITUTE OF PRIMATE RESEARCH (IPR) AT KAREN

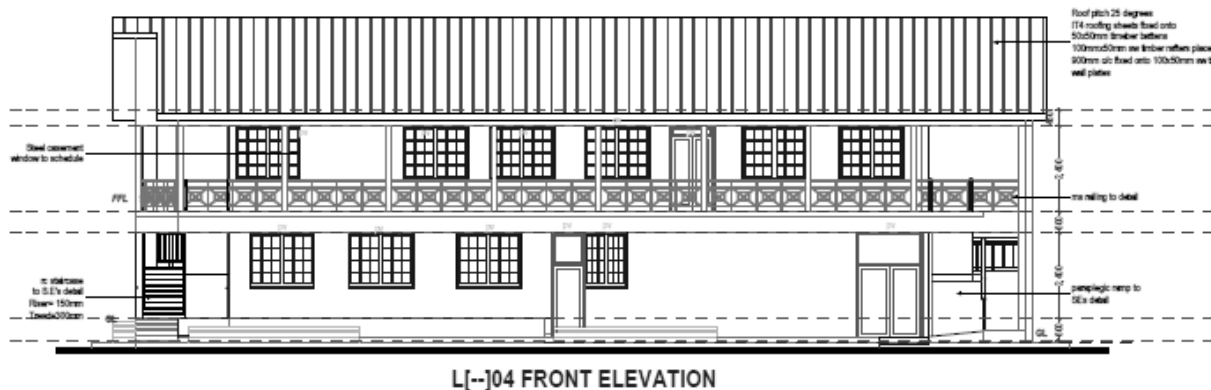

Interim Architect Penultimate Payment Certificate No. 09

Quantity Surveyors:

Integrity Quantity Surveyors
P.O. BOX 15521-00100,
Nairobi

Services Engineers:

Plancad Associates
P.O. BOX 67605 -00100
Nairobi

Architects:

Archscan Associates Limited
P.O. BOX 10958 -00100
Nairobi

Civil & Structural Engineers:

Pharma Consulting Engineers
P.O. BOX 16505 -00100
Nairobi

10th June, 2019

Completion Clearance



Institute of Primate Research

Address: P. O. Box 24481-00502 Karen Nairobi Kenya | Tel: +254 02 2606235 | Fax: +254 02 2606231
URL: www.primateresearch.org | Email: directoripr@primateresearch.org

Our Ref: SOD/COW/IPR/6/19

Date: 10th June, 2019

The Project Managers,
M/s Archscan Associates Limited
P.O. BOX 10958-00100,
Nairobi

Attention: Arch. Francis Macharia

Dear Sir,

RE: Proposed Resource Centre For The Institute of Primate Research Institute (IPR) , Karen
IPR Resource Centre Civil Works Sign Off /Maintenance Period

Above project and captioned matter refers.

On behalf of the Institute of Primate Research, the undersigned wishes to confirm that he has inspected the building with the Project Architects and Eadsons Construction Limited and confirm that the building is ready for use and has been executed as per to the contract specifications and therefore has no objection for commissioning and handing over by M/s Eadsons Construction Limited from above date when keys were handed over.

We further confirm that the works have been done and commissioned in line with the attached Contract Offer letter dated 16th November, 208 (Reference IPR/ADM/SUP/1.175) and contract conditions.

For purposes of Project Closure and documentation, the Contractual Six (6) Months Defects /Maintenance Liability Period may be noted as effective from date of this letter, 10th June, 2019 and shall lapse on 10th December, 2019 but the Contractor, copied herein, shall be expected to attend to any urgent items that may be flagged during maintenance period

Finally, and having certified the building as practically completed, we request the Project Architects to proceed and issue to M/s Eadsons Construction Limited the Certificate of Practical Completion and facilitate release of their 5 % Retention Moiety as provided for in Clauses 34.0 & 41.0 of the Agreement & Conditions of Contract for Building Works.

Yours Faithfully,
Clerks of Works

 10/6/2019.

Smith Itila

INSTITUTE OF PRIMATE RESEARCH

Completion/Handover Minutes

Our Ref: MP/38/Post Graduate Training & Resource Centre/ Completion Minutes /10

Date: 10th June, 2019

The Director,
Institute of Primate Research,
The National Museums of Kenya,
P.O. BOX 24481-00502,
Nairobi

Attention: Dr Hastings Ozwara,

Dear Sir,

RE: Proposed Post Graduate Training & Resource Centre For The Institute of Primate Research (IPR) , on Plot L.R. NO. 23268 at Karen, Nairobi County

Minutes of Project Handover Meetings No.10 Held on Monday, 10th June, 2019 at 9.00 am

Kindly see hereunder project completion minutes of our above captioned meeting for your records.

Attendance List

	Name	Firm	Tel	Email	Action
1.	Dr Hastings	Institute of Primate Research	0721 483 326	'ozwara@museums.or.ke'	IPR
2.	Lillian C. Maheli	Institute of Primate Research	0722 857 836	lillycham@yahoo.com	IPR
3.	Elikanah M Ragoi	Eadsons Construction Limited	0722 818 131	Muhiaragoi87@gmail.com	K A
4.	Kahethu FK	Institute of Primate Research	0723 717 302	lillycham@yahoo.com	IPR
5.	Miriam Kamuira	Institute of Primate Research	0725 934 896	miriam@primateresearch.org	IPR
6.	Zeruya Opiyo	Institute of Primate Research	0721 609 730	Zeruya.opiyo@gmail.com	
7.	Simon Komen	Institute of Primate Research	0722 563 328	'skomen@museums.or.ke'	
8.	Grace Mathini	Institute of Primate Research			IPR
9.	Lucyline Mbogori	Institute of Primate Research		lucymbogori@gmail.com	
10.	Peter Okwaro	Institute of Primate Research			
11.	Jane Demba	Institute of Primate Research			
12.	Smith Itila	Institute of Primate Research	0722 682 791	'Sitila@primateresaerch.org'	
13.	Ezekiel Matitu	Wingu Solutions Limited	0719 268 018	ezeziel.matito@gmail.com	
14.	Francis Macharia	Archscan Associates Limited	0722 376 969	archscan@archscanassociates.com	AAL

PROJECT DATA SHEET

Client : INSTITUTE OF PRIMATE RESEARCH , P.O. BOX 24481-00502 KAREN., NAIROBI	
Main Contractor : EADSONS CONSTRUCTION LIMITED P.O. BOX 11042-00400 , NAIROBI	
DOMESTIC SUB-CONTRACTORS:	CONSULTANTS CONSORTIUM
Electrical Sub-Contractor :	Project Managers/Architect
Structured Cabling Sub-Contractor	Quantity Surveyors
Others (Specify)(Roofing):	Services Consultants
	Structural Engineers
	Archscan Associates Limited
	Integrity Quantity Surveyors
	Plancad Associates
	Pharma Consulting Engineers

MATTERS ARISING

Ref	Item	Remarks	Time	Action
Snag /10/01	Opening Prayers/ Previous Minutes	Opening Prayers were done by Simon Komen.		Info
Snag /10/02	Meeting Agenda	The Meeting had been called by the Client for Formal Project Handover by the Contractor with below Agenda Items		Info
	CONTRACTORS/SUB CONTRACTORS ISSUES			
Snag /10/03	Gents Keys	Contractor to attend to the faulty Gents toilet door lock		Eadsons COW
Snag /10/04	Fire Alarm Surface Trunking	Contractor to conceal the exposed surface trunking at the reception and Office No.01		Eadsons
Snag /10/05	Glazing Film	Contractor to attend to the glazing fixing to eliminate air bubbles		Eadsons
Snag /10/06	Glazing Cleaning	Contractor to ensure all putty/finger prints are removed from glazing		Eadsons
Snag /10/07	Paraplegic Washrooms	Contractor to install missing handles and accessories to make the Paraplegic washroom functional		Eadsons
Snag /10/08	Grouting	Contractor to ensure all tiles are clean and grouting done uniformly		Eadsons
Snag /10/09	Aluminium Locks	The Client confirmed that they will make direct purchases for sanitary fittings and discount the price from the Contract		Eadsons
Snag /10/10	Meter Board	Contractor to note that the meter board in the store does not meet the required standard and it will be redone during ablution works		Eadsons
Snag /10/11	Hooks /Doors Stoppers	Contractor to provide restraining hooks and door stoppers to all external main metal doors		Eadsons
Snag /10/12	Exposed Wires	Contractor to ensure all naked wires/exposed outlets are insulated for safety of uses		Eadsons
Snag /10/13	Armored Cable Marking	Contractor to clearly mark area where armored cable was installed using hatari blocks		Eadsons
Snag /10/14	Gate Valves	Contractor to indicate where al water gate valves were installed		Eadsons
Snag /10/15	Water Reticulation	This will be done by the Client during ablution Construction		Eadsons
Snag /10/16	Landscaping Works	The Client will undertake landscaping completion on their own		Eadsons
Snag /10/17	Structured Cabling	Wingu Solutions were requested to be on standby for any challenges that might arise from heir installation		
Snag /10/18	Site Debris/Cleaning	Contractor to proceed with the removal of all construction debris and clean premises		Eadsons
	CLIENT ISSUES			
Snag /10/19	Landscaping	Client to undertake landscaping in house		IPR
Snag /10/20	Furniture	Client to undertake furniture sourcing and procurement in house		IPR
Snag /10/21	Curtains	Client to undertake curtains selection, sourcing and procurement in house		IPR
Snag /10/22	Monitors/Speakers	Client to undertake TV Monitors/Aerials/Speakers etc sourcing and procurement in house		IPR Wingu
Snag /10/23	Inverter	Client to review Wingu quotation for the Inverter System and advise on procurement		IPR Wingu
Snag /10/24	Air Conditioner	Client to review Wingu quotation for the Air Conditioner and advise on procurement		
Snag /10/25	ICT Installations	Client / Wingu to agree on other pending ICT installations		Wingu
Snag /10/26	Signage	Client/Architect will agree on signage schedule for installation (washrooms, offices, conference hall etc)		IPR
Snag /10/27	Foldable Partition	Client/Architect will agree on foldable aluminium partition details for the big conference room on first floor		IPR Archscan
Snag /10/28	Fire Extinguishers	Client to install fire extinguishers / fire blanket to comply with safety requirements		IPR
Snag /10/29	Rainwater Harvesting	Client /Architect will agree on rainwater harvesting/reticulation during ablution construction		IPR Archscan

Snag /10/30	Hose Reel /Pumps	Client /Architect will agree on Hose reel / pumps installation during ablution construction		IPR Archscan
Snag /10/31	Fire Escape Map	Client /Architect to agree on fire escape routes / fire maps		Archscan
	ANY OTHER BUSINESS			
Snag /10/32	Handover Report	The Clerks of Works/Architects shall prepare a joint project handover/commissioning report		COW Archscan
Snag /10/33	Completion Date /	It was agreed that the effective date for handover/Practical completion shall be noted as Monday, 10th June, 2019		Info
Snag /10/34	Defects Liability Period	The Contractual Six (6) Months Defects Liability Period shall lapse on Tuesday 10th December, 2019		Info
Snag /10/35	Keys Handover	The Contractors/Clerks of Works shall prepare a keys schedule and plan for handover of all keys		COW Eadsons
Snag /10/36	COW Signoff	The Clerks of Works shall prepare a sign off letter for purposes of project handover		COW Eadsons
Snag /10/37	Training	Wingu/Eadsons to ensure Users are trained on all ICT installations in the building and to offer back up support during the 6 Months Maintenance Period		COW Eadsons Wingu
Snag /10/38	Completion Certificate Retention /	The Architect will prepare and issue Certificate of Practical completion to Eadsons Construction Limited to facilitate release of their 5 % Retention Moiety		Archscan Eadsons IPR
Snag /10/39	Draft Final Accounts	The Contractor to liaise with the Quantity Surveyors/Services Engineers for Draft Final Accounts sign off		Archscan IQS
Snag /10/40	Installation Drawings	Project Architect /Services Engineers will prepare and submit as built/installation drawings on project completion		Archscan Plancad
Snag /10/41	Penultimate Payment No.09	Consultants will prepare and issue Penultimate Payment No.09 for settlement by the Client		I Archscan IQS
Snag /10/42	Wingu Penultimate Payment	The Architect confirmed that Penultimate Payment No.01 for Wingu had been issued for settlement		Archscan IPR
Snag /10/43	Next Site Meeting	Next Site Meeting will be held on Notice		Info

Signed on Confirmation of Minutes

1.Name.....Designation.....SignDate
On behalf of **Client / Institute of Primate Research**

2.Name.....Designation.....SignDate
On behalf of **Project Managers/ Archscan Associates**

3.Name.....Designation.....SignDate
On behalf of **Structured Cabling Sub Contractors/ Wingu Solutions Limited**

4.Name.....Designation.....SignDate
On behalf of **Contractors/ Eadsons Construction Limited**

Certificate of Practical Completion



Rose Avenue off Ngong Road P.O.Box 10958 GPO-00100 NAIROBI
Tel: +254 20 2736388/91, 020 2015662 Fax: +254 20 2728507, 020 2015662
Email: archscan@archscanassociates.com / Website: www.archscanassociates.com

PIN NO. P05121080E
VAT NO. 0125254F

~~CERTIFICATE OF PRACTICAL COMPLETION~~
~~CONSULTING ARCHITECTS~~ ~~INTERIOR DESIGNERS~~ ~~PROJECT MANAGERS~~

Our Ref: MP/38/IPR Resource Centre / Certificate of Practical Completion /2019

Date: Monday, 10th June, 2019

M/s Eadsons Construction Limited

P.O. BOX 11042-00400,

Nairobi

Attention: Elikanah Muhia Ragoi,

Dear Sirs,

RE: Proposed Post Graduate Training & Resource Centre For The Institute of Primate Research (IPR) , on Plot L.R. NO. 23268 at Karen, Nairobi County

Certificate of Practical Completion

This Practical Completion Certificate is issued following completion of the above mentioned project on the above indicated date. The summary of the Project Particulars are as below:

Contract Date : Wednesday, 28th November, 2018

Date of Practical Completion : Monday, 10th June, 2019

Final Contract Sum : Kshs 14,742,679.00

Job Name : Proposed Post Graduate Training & Resource Centre For the Institute of Primate Research (IPR)

**Employers Name : Institute of Primate Research /the National Museums of Kenya,
P.O. BOX 24481-00502, Karen Nairobi**

Main Contractors Name: M/s Eadsons Construction Limited P.O. BOX 11042-00400, Nairobi

In accordance with **Clause 41.2** of the Agreement and Conditions of Contract for Building Works (1999 EDITION), we hereby certify that the above mentioned Project was completed to our satisfaction and taken into possession by the Client /Users effective from **Monday, 10th June, 2019**

This Certificate of Practical Completion is issued subject to making good by the Main Contractor of any outstanding defects, shrinkages and other faults which may appear during the six (6) months Defects Liability Maintenance Period as provided for in Sub Clauses 41.6, 41.7 & 41.9 of the Contract.

Finally, following the aforesaid Practical Completion Certification and attached Client letter dated **10th June, 2019** (Reference SOD/COW/IPR/6/19), We hereby recommend that one moiety of the retention monies (5%) deducted under all previous Architect's Interim Payment Certificates (No. 01-08) in respect of the said works be released to the Main Contractor and as computed in the attached Penultimate Valuation No.09.

Defects Liability/Maintenance Period Expiry Date : Tuesday 10th December, 2019

Signed _____ (Official Stamp): _____
ARCHSCAN ASSOCIATES LIMITED

Circulation

**The Director,
Institute of Primate Research,
The National Museums of Kenya,
P.O. BOX 24481-00502,
Nairobi**

Attention: Dr Hastings Ozwara,

**Integrity Quantity Surveyors
P.O. BOX 15521-00100,
Nairobi**

Attention: QS Peter Ndungu,

**Pharma Consulting Engineers
P.O. BOX 16505-00100
Nairobi**

Attention: Eng Josphat W Macharia,

**Plancad Services Engineers
P.O. BOX 67605-00100
Nairobi**

Attention: Eng Simon Ombwayo,

Penultimate Certificate No.09

Our Ref: MP/38/Architect Penultimate Payment Certificate /09

Date: 10th June, 2019

The Director,
Institute of Primate Research,
The National Museums of Kenya,
P.O. BOX 24481-00502,
Nairobi

Attention: Dr Hastings Ozwara,

Dear Sir,

RE: Proposed Post Graduate Training & Resource Centre For The Institute of Primate Research (IPR) , on Plot L.R. NO. 23268 at Karen, Nairobi County

Penultimate Payment Certificate No.09

Following project Practical Completion and Handover on 10th June, 2019 and further to your Award Letter dated 16.11.2018 (**Reference IPR/ADM/SUP/1.175**) for Phase 2 Works and Pursuant to Clause 34.0 of the Building Contract (*Agreement and Conditions of Contract for Building Works*), please find attached herewith Architect's Penultimate Payment **Certificate No. 09** for **Kshs 1,859,855.60** (*Shillings One Million, Eight Hundred Fifty Nine Thousands, Eight Hundred Fifty Five and Sixty Cents Only*) Payable to **M/s Eadsons Construction Limited** for works done and valued up to date and as specifically itemized in the attached summary of the attached Quantity Surveyors Penultimate Valuation No. 09 (*dated 31st May, 2019 Reference IQS/Resource Centre/penultimate Valuation /09*) and the associated cost build ups for your record.

Table 1: Penultimate Payment Certificate No.09

	Item	Amount/Kshs	Notes
1	Preliminaries	815,000.00	<i>See attached Quantity Surveyors Penultimate Valuation No. 09 (dated 31st May, 2019 Reference IQS/Resource Centre/Penultimate Valuation /09)</i>
2	Main Building	12,468,245.00	
3	Materials on Site	0.00	
4	Electrical Installations	934,589.00	<i>See attached Electrical Services Final Account</i>
5	Mechanical Installations	524,845.00	<i>See attached Plumbing Services Final Account</i>
6	GROSS PENULTIMATE VALUATION 09 / DRAFT FINAL ACCOUNT	14,742,679.00	
7	Less Previous payments PHASE 1	7,626,285.00	<i>(Certificates No.01-04)</i>
8	Gross valuation PHASE 2	7,116,394.00	
9	Less 5% retention	355,819.70	Payable after Six (6) Months Defects Liability Period expiry on 7.12.2019
10	Amount Due	6,760,574.30	
11	Less Previous payments (PHASE 2)		
12	Less Amount Paid in Certificate No.05	1,044,085.50	<i>Certificate S/No. 1017842 dated 10.12.2018</i>
13	Less Amount Paid in Certificate No.06	885,735.00	<i>Certificate S/No. 1017845 dated 10.01.2019</i>
14	Less Amount Paid in Certificate No.07	1,138,412.70	<i>Certificate S/No. 1017846 dated 30.01.2019</i>
14	Less Amount Paid in Certificate No.08	1,155,583.50	<i>Certificate S/No. 1012902 dated 18.03.2019</i>
15	Total Amount Valued	4,223,816.70	
16	Amount Payable to Contractor	2,536,757.60	
17	Less Ceramics Tiles Purchases (Proforma Invoice No.01)	366,642.00	

18	Less Ceramics Tiles Purchases (Proforma Invoice No.02)	310,260.00	
19	Penultimate Amount Payable to Contractor in Valuation No. 09	1,859,855.60	<i>Certificate S/No. 1012907 dated 7.06.2019</i>
15	Less 3 % With Holding Tax	48,099.71	PIN NO. P 051190401 D
16	Amount Payable to Contractor in Penultimate Valuation No. 09	1,811,755.89	

Shillings One Million, Eight Hundred Eleven Thousands, Seven Hundred Fifty Five and Ninety Cents Only

Table 2: Summary of Payment Certificates


	Cert No.	Certificate Value	Notes
1	Cert No.01	2,730,758.00	<i>Certificate S/No. 971337 dated 13.11.2013</i>
2	Cert No.02	1,738,255.50	<i>Certificate S/No. 984102 dated 7.01.2014</i>
3	Cert No.03	1,809,783.00	<i>Certificate S/No. 984115 dated 14.03.2014</i>
4	Cert No.04	1,347,488.50	<i>Certificate S/No. 1017837 dated 13.11.2018</i>
5	Cert No.05	1,044,085.50	<i>Certificate S/No. 1017842 dated 10.12.2018</i>
6	Cert No.06	885,735.01	<i>Certificate S/No. 1017845 dated 10.01.2019</i>
7	Cert No.07	1,138,412.01	<i>Certificate S/No. 1017846 dated 30.01.2019</i>
8	Cert No.08	1,155,812.01	<i>Certificate S/No. 1012902 dated 18.03.2019</i>
9	Cert No.09	1,859,855.60	<i>Certificate S/No. 1012902 dated 18.03.2019</i>
10	Add Ceramics Tiles Purchases (Proforma Invoice No.01)	366,642.00	<i>Paid By the Client/Institute of Primate Research (IPR)</i>
11	Add Ceramics Tiles Purchases (Proforma Invoice No.02)	310,260.00	<i>Paid By the Client/Institute of Primate Research (IPR)</i>
12	Add Retention Sum	355,819.70	<i>Payable after expiry of Six (6) Months Maintenance Period on 10.12.2019</i>
13	Final Account Statement	14,742,906.80	

Shillings Fourteen Million Seven Hundred Forty Two Thousands Nine Hundred Six and Eighty Cents Only

In the meantime, and as per the Client Sign Off letter dated 10th June, 2019 (Reference SOD/COW/IPR/6/19), and having certified the building as practically completed, please find attached herewith the Certificate of Practical Completion dated 10th June, 2019 (Reference MP/38/IPR Resource Centre / Certificate of Practical Completion /2019) to facilitate the release of 5 % Retention Moiety to M/s Eadsons Construction Limited as provided for in Clauses 34.0 & 41.0 of the Agreement & Conditions of Contract for Building Works

Finally, and by Copy of this letter and pursuant Clause 34.0 and specifically sub Clause 34.23 of the Agreement and Conditions of Contract for Building Works, the Contractor, is requested to note that the Consultants/Client reserves the right to adjust the amount certified herein from any subsequent payments should the works be confirmed not to have been undertaken to the required contract standards and specifications or in absence of approval of material tests by the Structural Engineers (concrete, stones, aggregates etc).

Yours Faithfully



Francis Macharia

ARCHSCAN ASSOCIATES LIMITED

Circulation

M/s Eadsons Construction Limited
P.O. BOX 11042-00400,
Nairobi

Attention: Elikanah Muhia Ragoi,

Integrity Quantity Surveyors
P.O. BOX 15521-00100,
Nairobi

Attention: QS Peter Ndungu,



Serial No. 1012907

INTERIM CERTIFICATE

Job no MP/38/2018
 Job name IPR RESOURCE CENTRE
 Employer's name NATIONAL MUSEUMS OF KENYA / INSTITUTE OF PRIMATE RESEARCH (IPR)
 Address P.O. BOX 24481-00502, NRB
 Contractor's name EADSONS CONSTRUCTION LTD
 Address P.O. Box 110402-00400 NRB
 I/we hereby certify that the sum of shillings ONE MILLION, EIGHT HUNDRED FIFTY NINE THOUSANDS, EIGHT HUNDRED FIFTY FIVE AND SIXTY CENTS ONLY =
 KES 1,859,855/60

is due to the contractor from the employer under terms of the contract on account of work carried out and/or materials supplied.

FRANCIS MACHARIA

NAME OF ARCHITECT / FIRM

Issue Date 10TH JUNE, 2019
 Certificate No PENULTIMATE-09
 Contract Date 28TH NOV, 2018 (PHASE 2)
 Contract Sum KES PHASE 1 - 7,626,285/00
PHASE 2 - 7,116,394/00
TOTAL 14,742,679
 Present Instalment KES 1,859,855/60
 Previous Instalment KES 4,223,816/70
 Total Certified KES 6,083,672/30
 Retention KES 355,819/70

A8481807BORAQS
Registration No.AAK
Membership No.**CONTRACTOR'S RECEIPT**

Received from _____
 The sum of KES _____
 In payment of cert. no _____ Date _____
 The sum of KES _____

Serial No 1012907

Date _____

STAMP



INTEGRITY QUANTITY SURVEYORS

Registered Quantity Surveyors, Property Valuations & Project Management

P.O. BOX 15521-00100, Tel 0722 670570 Nairobi Email: peter.ndung@yahoo.com

Our Ref: IQS/Resource & Training Centre /Penultimate Valuation /09

Date: 31st May, 2019

**Archscan Associates Limited,
P.O. BOX 10958 -00100
NAIROBI**

Dear Sirs,

RE: Proposed Post Graduate Training & Resource Centre For The Institute of Primate Research (IPR) , on Plot L.R. NO. 23268 at Karen, Nairobi County

Penultimate Valuation Statement No. 09

Please see attached summary of Penultimate Valuation No. 09 based on site re-measurements and Contract Bills of Quantities tender rates following our site visit on 28th May, 2019. We recommend that the below indicated amount of **Kshs 1,859,855.60** (*Shillings One Million, Eight Hundred Fifty Nine Thousands, Eight Hundred Fifty Five and Sixty Cents Only*) be payable to **M/s Eadsons Construction Limited**

Table 1: Summary Penultimate Valuation Statement No. 09


	Item	Amount/Kshs	Notes
1	Preliminaries	815,000.00	<i>See attached Quantity Surveyors Penultimate Valuation No. 09 (dated 31st May, 2019 Reference IQS/Resource Centre/Penultimate Valuation /09)</i>
2	Main Building	12,468,245.00	
3	Materials on Site	0.00	
4	Electrical Installations	934,589.00	<i>See attached Electrical Services Final Account</i>
5	Mechanical Installations	524,845.00	<i>See attached Plumbing Services Final Account</i>
6	GROSS PENULTIMATE VALUATION 09 / DRAFT FINAL ACCOUNT	14,742,679.00	
7	Less Previous payments PHASE 1	7,626,285.00	<i>(Certificates No.01-04)</i>
8	Gross valuation PHASE 2	7,116,394.00	
9	Less 5% retention	355,819.70	Payable after Six (6) Months Defects Liability Period expiry on 7.12.2019
10	Amount Due	6,760,574.30	
11	Less Previous payments (PHASE 2)		
12	Less Amount Paid in Certificate No.05	1,044,085.50	<i>Certificate S/No. 1017842 dated 10.12.2018</i>
13	Less Amount Paid in Certificate No.06	885,735.00	<i>Certificate S/No. 1017845 dated 10.01.2019</i>
14	Less Amount Paid in Certificate No.07	1,138,412.70	<i>Certificate S/No. 1017846 dated 30.01.2019</i>
14	Less Amount Paid in Certificate No.08	1,155,583.50	<i>Certificate S/No. 1012902 dated 18.03.2019</i>

15	Total Amount Valued	4,223,816.70	
16	Amount Payable to Contractor	2,536,757.60	
17	Less Ceramics Tiles Purchases (Proforma Invoice No.01)	366,642.00	
18	Less Ceramics Tiles Purchases (Proforma Invoice No.02)	310,260.00	
19	Penultimate Amount Payable to Contractor in Valuation No. 09	1,859,855.60	<i>Certificate S/No. 1012907 dated 10.06.2019</i>

Shillings One Million, Eight Hundred Fifty Nine Thousands, Eight Hundred Fifty Five and Sixty Cents Only

By Copy of this letter and pursuant Clause 34.0 and specifically sub Clause 34.23 of the Agreement and Conditions of Contract for Building Works, the Contractor, is requested to note that the Consultants/Client reserves the right to adjust the amount certified herein from any subsequent payments should the works be confirmed not to have been undertaken to the required contract standards and specifications or in absence of approval of material tests by the Structural Engineers (concrete, stones, aggregates etc).

Yours Faithfully



QS Peter Ndungu
For: Integrity Quantity Surveyors

Circulation

The Client

**The Director,
Institute of Primate Research,
The National Museums of Kenya,
P.O. BOX 24481-00502,
Nairobi**

Attention: Dr Hastings Ozwara,

The Contractor

**The Director,
M/s Eadsons Construction Limited
P.O. BOX 11042-00400,
Nairobi**

Attention: Elikanah Muhia Ragoi,

Services Engineers:

**Plancad Associates
P.O. BOX 67605 -00100
Nairobi**

Attention: Eng Simon Ombwayo

Contractors Final Account Concurrence



EADSONS CONSTRUCTION & ENGINEERING COMPANY



Braidwood House ,2nd Floor
Tom Mboya Street
P. O. BOX 11042-00400

Email:eadsons@yahoo.com
Mobile: 0722 818131

Archscan Associates Limited,
P.O. BOX 10958 -00100
NAIROBI

Attention: Architect Francis Macharia
Dear Sirs,

RE: Proposed Post Graduate Training & Resource Centre For The Institute of Primate Research (IPR) , on Plot L.R. NO. 23268 at Karen, Nairobi County

Penultimate Payment Certificate No.09/Draft Final Account

The above project and captioned subject matter refers

We confirm and concur with the Draft Final Account for the above project as extracted from the Quantity Surveyors Penultimate Valuation No. 09 (dated 31st May, 2019 Reference IQS/Resource Centre/penultimate Valuation /09) and as below summarized in Table 1;

Table 1: Draft Final Account Statement

	Certificate No.	Certificate Value	Notes
1	Cert No.01	2,730,758.00	Certificate S/No. 971337 dated 13.11.2013
2	Cert No.02	1,738,255.50	Certificate S/No. 984102 dated 7.01.2014
3	Cert No.03	1,809,783.00	Certificate S/No. 984115 dated 14.03.2014
4	Cert No.04	1,347,488.50	Certificate S/No. 1017837 dated 13.11.2018
5	Cert No.05	1,044,085.50	Certificate S/No. 1017842 dated 10.12.2018
6	Cert No.06	885,735.01	Certificate S/No. 1017845 dated 10.01.2019
7	Cert No.07	1,138,412.01	Certificate S/No. 1017846 dated 30.01.2019
8	Cert No.08	1,155,812.01	Certificate S/No. 1012902 dated 18.03.2019
9	Cert No.09	1,859,855.60	Certificate S/No. 1012902 dated 18.03.2019
10	Add Ceramics Tiles Purchases (Proforma Invoice No.01)	366,642.00	Paid By the Client/Institute of Primate Research (IPR)
11	Add Ceramics Tiles Purchases (Proforma Invoice No.02)	310,260.00	Paid By the Client/Institute of Primate Research (IPR)
12	Add Retention Sum	355,819.70	Payable after expiry of Six (6) Months Maintenance Period on 7.12.2019
13	Final Account Statement/Draft Final Account	14,742,906.80	

Shillings Fourteen Million Seven Hundred Fourty Two Thousands Nine Hundred Six and Eighty Cents Only

We further confirm that we shall be on call during the Six (6) Months Defects Liability Period and as per the attached Certificate of Practical Completion dated 10th June, 2019 (Reference MP/38/IPR Resource Centre / Certificate of Practical Completion /2019)

Yours Faithfully

Elikanah Muhia Ragoi,
EADSONS CONSTRUCTION LIMITED

Circulation

**The Director,
Institute of Primate Research,
The National Museums of Kenya,
P.O. BOX 24481-00502,
Nairobi**

Attention: Dr Hastings Ozwara,

**Integrity Quantity Surveyors
P.O. BOX 15521-00100,
Nairobi**

Attention: QS Peter Ndungu,



**Detailed Civil Works Contract Draft Final Account
Re-Measurements Bills of Quantities/**

PRELIMINARIES

1.00

ITEM	DESCRIPTION	CONTRACT VALUE	INITIAL PAYMENT	WEEKLY PAYMENT	FINAL/REMOVAL
	Insurances	100,000.00	100,000.00		
	Performance Bond	75,000.00	75,000.00		
	Training Levy	50,000.00	50,000.00		
	Standards Levy	50,000.00	50,000.00		
	Electricity for the works	50,000.00	10,000.00	2,500.00	
	Water for the works	50,000.00	10,000.00	2,343.75	2,500.00
	Storage sheds for materials	50,000.00	10,000.00	2,343.75	2,500.00
	Security of the works	50,000.00	10,000.00	2,343.75	2,500.00
	Health and safety	250,000.00	50,000.00	12,500.00	
	Site Office	90,000.00	18,000.00	4,218.75	4,500.00
	Total	815,000.00	383,000.00	26,250.00	12,000.00
	Valuation No. 9				
	Initial	383,000.00			
	Weekly x 16 Weeks	420,000.00			
	Final	12,000.00			
	Amount due carried to summary	815,000.00			

MAIN BUILDING

ITEM	DESCRIPTION	Bq Qty	Done	Unit	Bq Rate	Revised Rate	Bq Amount	Valuation
	<u>SUBSTRUCTURES (PROVISIONAL) :-</u>							
	<u>Page 1</u>							
A.	Site clearance to remove grass, shrubs, bushes and small trees	362	362	SM	25	25	9,050.00	9,050.00
B	Excavate to reduce levels not exceeding 1.50 M	362	145	CM	280	280	101,360.00	40,600.00
C	Excavate trenches for strip foundations not exceeding 1.50 M	46	32	CM	280	280	12,880.00	8,960.00
D	Ditto for column bases ditto	43	29	CM	280	280	12,040.00	8,120.00
E	Load cart away or spread extra excavation material on site	422	153	CM	400	400	168,800.00	61,200.00
F	Return in, fill and ram well selected excavation materials	48	53	CM	150	150	7,200.00	7,950.00
G	Extra over excavation for rock excavation	113	29	CM	1,800	1,800	203,400.00	52,200.00
	<u>Filling</u>							
H	Selected hardcore filling under ground slab	92	92	CM	1,100	1,100	101,200.00	101,200.00
I	50 mm thick murrum or quarry dust blinding to hardcore	230	230	SM	150	150	34,500.00	34,500.00
J	500 gauge damp proof membrane	230	230	SM	80.00	80.00	18,400.00	18,400.00
K	Chemical anti-termite treatment	230	230	SM	240.00	240.00	55,200.00	55,200.00
	<u>Plain concrete (1:4:8) as described in :-</u>							
A	50 mm thick under strip foundations	39	64	SM	400	400	15,600.00	25,600.00
B	50 mm thick under column bases	29	51	SM	400	400	11,600.00	20,400.00
	<u>Vibrated Reinforced Concrete class 20 in :-</u>							
C	Strip foundations	8	13	CM	11,000	11,000	88,000.00	143,000.00
D	Column bases	12	27	CM	11,500	11,500	138,000.00	310,500.00
E	Columns	2	2	CM	11,500	11,500	23,000.00	23,000.00
F	100 mm floor slab	230	230	SM	1,100	1,100	253,000.00	253,000.00
	<u>High Tensile Reinforcement Bars to B. S. 4461</u>							
G	Assorted reinforcement bars estimated at 75 Kg/CM	1,760	1,760	KG	140	140	246,400.00	246,400.00
	<u>Mesh fabric reinforcement</u>							
H	B. R. C. A 142 mesh reinforcement to Engineers specification	230	230	SM	400	400	92,000.00	92,000.00
	<u>Sawn formwork as described to :-</u>							
I	Sides of strip foundations	26	43	SM	200	200	5,200.00	8,600.00
J	Sides of column bases	35	59	SM	400	400	14,000.00	23,600.00
K	Sides of columns	25	22	SM	400	400	10,000.00	8,800.00
L	Edges of slab 75 mm - 150 mm high	65	65	LM	60	60	3,900.00	3,900.00
	<u>Natural stone walling bedded and jointed in mortar</u>							
M	200 mm thick	77	130	SM	1,680	1,680	129,360.00	218,400.00
	<u>Cement and sand 1:4 screed, wood floated</u>							
A	15 mm thick to plinth	26	26	SM	280	280	7,280.00	7,280.00
	<u>50 mm thick random rubble stone walling</u>							
B	Plinth surface	26	0	SM	800	800	20,800.00	-
*	Two coats black bituminous paint to plinth	0	26	SM	150	150	-	3,900.00
	<u>Items</u>							
C	Allow for keeping excavations clear of all water			ITEM			5,000.00	5,000.00
D	Allow for plunking and strutting to support sides of excavation			ITEM			5,000.00	5,000.00
	<u>Trees</u>							
*	Cutting trees girth exceeding 300 mm and grubbing up roots	0	60	No	1,500	1,500	-	90,000.00
	<u>Paving Slabs</u>							
*	600 x 600 x 50 mm PCC paving slabs incl. hardcore & excavation	0	95	SM	1,050	1,050	-	99,750.00
*	Landscaping (ground preparation and grassing)	0	513	SM	650	200	-	102,600.00
	Total carried to Summary						1,792,170.00	2,088,110.00

ITEM	DESCRIPTION	Bq Qty	Done	Unit	Bq Rate	Revised Rate	Bq Amount	Valuation
ELEMENT NO. 2								
R. C. SUPERSTRUCTURE (GROUND FLOOR)								
Reinforced Concrete class 20 as described to :-								
A	Beams	13	13	CM	11,500	11,500	149,500.00	149,500.00
B	Columns	5	5	CM	11,500	11,500	57,500.00	57,500.00
C	Staircase	2	2	CM	11,500	11,500	23,000.00	23,000.00
D	150 mm suspended slab	51	51	SM	1,650	1,650	84,150.00	84,150.00
E	175 mm thick ramp	36	36	SM	1,725	1,725	62,100.00	62,100.00
F	175 mm thick landings	15	15	SM	1,725	1,725	25,875.00	25,875.00
Hollow pot suspended slab								
G	300 mm thick hollow pot slab	152	152	SM	1,750	1,750	266,000.00	266,000.00
Mesh fabric reinforcement								
H	B. R. C. A 142 mesh reinforcement to Engineers specification	152	152	SM	400	400	60,800.00	60,800.00
High Tensile Reinforcement Bars to B. S. 4461								
I	Assorted reinforcement bars estimated at 90 Kg/CM	6,110	6,110	KG	140	140	855,400.00	855,400.00
Sawn Formwork as described to :-								
J	Sides and soffits of beams	164	164	SM	400	400	65,600.00	65,600.00
K	Sides of columns	67	67	SM	400	400	26,800.00	26,800.00
L	Soffit of suspended slab	203	203	SM	400	400	81,200.00	81,200.00
A	Soffit of suspended landings	15	15	SM	400	400	6,000.00	6,000.00
B	Sloping soffit of staircase	9	9	SM	400	400	3,600.00	3,600.00
C	Sloping soffit of ramp	36	36	SM	400	400	14,400.00	14,400.00
D	Edges of suspended slab 75 mm - 150 mm girth	60	60	LM	60	60	3,600.00	3,600.00
E	Edges of ramp 75 mm - 150 mm girth	56	56	LM	60	60	3,360.00	3,360.00
F	Edges of risers 75 mm - 150 mm girth	29	29	LM	60	60	1,740.00	1,740.00
G	Edges of staircase string 300 mm extreme girth	6	6	LM	120	120	720.00	720.00
R. C. SUPERSTRUCTURE (FIRST FLOOR)								
Reinforced Concrete class 20 as described to :-								
A	Beams	9	9	CM	11,500	11,500	103,500.00	103,500.00
B	Columns	4	4	CM	11,500	11,500	46,000.00	46,000.00
High Tensile Reinforcement Bars to B. S. 4461								
I	Assorted reinforcement bars estimated at 90 Kg/CM	1,170	1,170	KG	140	140	163,800.00	163,800.00
Sawn Formwork as described to :-								
J	Sides and soffits of beams	105	105	SM	400	400	42,000.00	42,000.00
K	Sides of columns	60	60	SM	400	400	24,000.00	24,000.00
Total carried to Summary							2,170,645.00	2,170,645.00
ELEMENT NO. 3								
WALLING - GROUND FLOOR								
External walling								
Machine cut 'Thika' stone walling								
A	200 mm thick external wall	145	145	SM	1,500	1,500	217,500.00	217,500.00
B	200 mm thick parapet wall	71	0	SM	1,500	1,500	106,500.00	-
Internal walling								
Machine cut 'Thika' stone walling								
C	200 mm thick	72	72	SM	1,500	1,500	108,000.00	108,000.00
D	100 mm thick	30	30	SM	1,200	1,200	36,000.00	36,000.00

ITEM	DESCRIPTION	Bq Qty	Done	Unit	Bq Rate	Revised Rate	Bq Amount	Valuation
	<u>Approved damp proof course</u>							
E	200 mm wide	84	84	LM	160	160	13,440.00	13,440.00
F	100 mm wide	10	10	LM	80	80	800.00	800.00
G	Aluminium partitioning in aluminium frames 100 x 50 mm and glazed in 6 mm laminated clear glass	34	43	SM	10,000	10,000	340,000.00	430,000.00
	<u>WALLING - FIRST FLOOR</u>							
	<u>External walling</u>							
	<u>Machine cut 'Thika' stone walling</u>							
A	200 mm thick external wall	145	145	SM	1,500	1,500	217,500.00	217,500.00
	<u>Internal walling</u>							
	<u>Machine cut 'Thika' stone walling</u>							
C	200 mm thick	72	72	SM	1,500	1,500	108,000.00	108,000.00
D	100 mm thick	30	30	SM	1,200	1,200	36,000.00	36,000.00
G	Aluminium partitioning in aluminium frames 100 x 50 mm and glazed in 6 mm laminated clear glass	34	34	SM	10,000	10,000	340,000.00	340,000.00
	<u>Variations</u>							
	<u>Cutting opening in 200 mm stone walling</u>							
	Opening size 2400 x 2000 mm		1	NO	2,000	2,000	-	2,000.00
	Opening size 1200 x 2800 mm		2	NO	1,400	1,400	-	2,800.00
	Opening size 1800 x 1100 mm		1	NO	800	800	-	800.00
	Opening size 900 x 500 mm		1	NO	200	200	-	200.00
	<u>Extra walling</u>							
*	200 mm thick machine cut stone walling		25	SM	1,500	1,500	-	37,500.00
	Total carried to Summary						1,523,740.00	1,550,540.00
	<u>ELEMENT NO. 4</u>							
	<u>ROOF</u>							
	<u>Mild Steel Roof Structure</u>							
	<u>Steel trusses to Engineer's details</u>							
A.	75 x 50 x 3 mm thick RHS rafters and tie beams	114	114	LM	1,200	1,200	136,800.00	136,800.00
B	50 x 50 x 3 mm thick SHS struts and ties	75	75	LM	960	960	72,000.00	72,000.00
C.	150 x 51 x 2 mm thick 'Z' purlins	256	256	LM	900	900	230,400.00	230,400.00
D	16 mm diameter round bar sag rods	40	40	LM	400	400	16,000.00	16,000.00
	<u>Wrot Cypress grade 1, planed</u>							
E	250 x 25 mm Fascia board	96	0	LM	490	490	47,040.00	-
	<u>Roof Covering</u>							
F	26 Gauge IT5 pre-painted roofing sheets	384	380	SM	1,950	1,950	748,800.00	741,000.00
G	450 mm matching ridge and hip cap	54	54	LM	600	600	32,400.00	32,400.00
H	450 mm matching valleys	10	10	LM	600	600	6,000.00	6,000.00
*	Supersisalation thermal insulation sheets		180	SM	550	550	-	99,000.00
*	Translucent roofing sheets		4	SM	2,000	2,000	-	8,000.00
	<u>Rainwater Disposal:-</u>							
	<u>24 Gauge SWG galvanized mild steel rainwater goods</u>							
A	150 x 150 mm rectangular boxed eaves gutter	80	72	LM	1,200	1,200	96,000.00	86,400.00
B	100 mm diameter rainwater downpipe imbedded to walls	60	48	LM	1,000	1,000	60,000.00	48,000.00
C	Ditto for 100 mm diameter outlets	10	8	NO	300	300	3,000.00	2,400.00
D	Extra over downpipe for 450 mm offsets	10	8	NO	450	450	4,500.00	3,600.00
E	Ditto for 450 mm discharging shoe	10	8	NO	300	300	3,000.00	2,400.00

ITEM	DESCRIPTION	Bq Qty	Done	Unit	Bq Rate	Revised Rate	Bq Amount	Valuation
	<u>Touch up primer prepare and apply three coats gloss oil paint</u>							
F	Surface of gutter	29	22	SM	290	290	8,410.00	6,380.00
G	Surfaces of large pipe	60	48	LM	29	29	1,740.00	1,392.00
	<u>Water Tank Platform to Engineer's details</u>							
*	75 x 50 x 3 mm thick RHS rafters and tie beams		18	LM	1,200	1,200	-	21,600.00
*	50 x 50 x 3 mm thick SHS struts and ties		10	LM	960	960	-	9,600.00
	Total carried to Summary						1,466,090.00	1,523,372.00
	<u>ELEMENT NO. 4</u>							
	<u>GROUND FLOOR FINISHES</u>							
	<u>Walls Finishes</u>							
A.	15 mm thick cement : sand (1:4) plaster to external surfaces	99	109	SM	300	360	29,700.00	39,240.00
B	Lime plaster to internal masonry or concrete surfaces	326	326	SM	310	400	101,060.00	130,400.00
C	15 mm plaster backing to receive wall tiles	94	82	SM	280	360	26,320.00	29,520.00
	<u>External Painting</u>							
	<u>Three coats "Duracoat" pure acrylic outdoor protector</u>							
D	External wall and concrete surfaces	99	109	SM	400	400	39,600.00	43,600.00
	<u>Key Pointing</u>							
E	10 mm half round neat horizontal joints in external walls	216	36	SM	180	300	38,880.00	10,800.00
	<u>Ceramic wall tiles</u>							
F	8 mm thick coloured ceramic wall tiles as "Saj Ceramics"	94	82	SM	1,500	1,800	141,000.00	147,600.00
	<u>Internal Painting</u>							
	<u>Three coats first quality silk vinyl matt paint to :-</u>							
G	Internal masonry or concrete surfaces	326	326	SM	260	300	84,760.00	97,800.00
	<u>Floors</u>							
	<u>Cement : sand (1:4) in :-</u>							
A	42 mm thick paving ready to receive ceramic tiles	230	168	SM	400	450	92,000.00	75,600.00
*	42 mm thick paving ready to receive granito tiles	0	41	SM	400	450	-	18,450.00
	<u>Ceramic floor tiles</u>							
B	10 mm thick Ceramic floor tiles as "Saj Ceramics"	230	168	SM	1,600	2,200	368,000.00	369,600.00
	<u>Skirtings</u>							
C	100 mm ceramic tile skirting	82	91	LM	240	240	19,680.00	21,840.00
	<u>Granito floor tiles</u>							
*	10 mm thick Granito floor tiles	0	41	SM	3,500	3,500	-	143,500.00
	<u>Ceiling finishes</u>							
	<u>Lime plaster as described to:-</u>							
D	Ceilings	203	133	SM	310	400	62,930.00	53,200.00
	<u>Three coats first quality silk vinyl matt paint to :-</u>							
G	Plastered ceilings	203	133	SM	260	300	52,780.00	39,900.00
	<u>Gypsum ceiling</u>							
*	9 mm gypsum ceiling including lightweight steel suspension		70	SM	2,200	2,200	-	154,000.00
*	75 mm gypsum cornice		120	LM	450	450	-	54,000.00
	<u>Three coats first quality plastic emulsion matt paint to :-</u>							
*	Gypsum ceiling		70	SM	300	300	-	21,000.00

ITEM	DESCRIPTION	Bq Qty	Done	Unit	Bq Rate	Revised Rate	Bq Amount	Valuation
	<u>Staircase and ramp finishes</u>							
	<u>Cement and sand (1:3) screed in:-</u>							
A	20 mm thick paving in landings	15	15	SM	200	360	3,000.00	5,400.00
B	20 mm thick paving in ramps	36	36	SM	200	360	7,200.00	12,960.00
C	20 mm thick paving in treads; 250 mm wide	28	28	LM	80	120	2,240.00	3,360.00
D	15 mm thick paving in risers; 150 mm high	29	29	LM	50	75	1,450.00	2,175.00
	<u>Lime plaster as described to:-</u>							
E	Soffit of suspended landings	15	15	SM	310	400	4,650.00	6,000.00
F	Sloping soffit of staircase	9	9	SM	310	400	2,790.00	3,600.00
G	Sloping soffit of ramp	36	36	SM	310	400	11,160.00	14,400.00
H	Edges of landings 75 mm - 150 mm girth	15	15	LM	50	90	750.00	1,350.00
I	Edges of ramp 75 mm - 150 mm girth	56	56	LM	50	90	2,800.00	5,040.00
H	Staircase string 300 mm wide extreme	6	6	LM	100	170	600.00	1,020.00
	<u>Three coats first quality silk vinyl matt paint to :-</u>							
J	Soffit of suspended landings	15	15	SM	260	300	3,900.00	4,500.00
K	Sloping soffit of staircase	9	9	SM	260	300	2,340.00	2,700.00
L	Sloping soffit of ramp	36	36	SM	260	300	9,360.00	10,800.00
M	Edges of landings 100 mm - 200 mm girth	15	15	LM	52	60	780.00	900.00
N	Edges of ramp 100 mm - 200 mm girth	56	56	LM	52	60	2,912.00	3,360.00
O	Staircase string 200 - 300 mm girth	6	6	LM	78	90	468.00	540.00
	<u>40 mm thick polished terrazzo laid onto :-</u>							
A	Landings	15		SM	2,500	2,500	37,500.00	-
B	Ramps	36		SM	2,500	2,500	90,000.00	-
C	Treads; 250 mm wide	28		LM	650	650	18,200.00	-
D	Risers; 150 mm high	29		LM	400	450	11,600.00	-
E	Skirtings; 100 mm high	15		LM	250	250	3,750.00	-
	<u>Granito floor tiles laid onto :-</u>							
*	Landings		15	SM	3,500	3,500	-	52,500.00
*	Ramps		36	SM	3,500	3,500	-	126,000.00
*	Treads; 250 mm wide		28	LM	900	900	-	25,200.00
*	Risers; 150 mm high		29	LM	550	550	-	15,950.00
*	Skirtings; 100 mm high		15	LM	350	350	-	5,250.00
	<u>Balustrading and railing</u>							
F	900 mm high mild steel staircase railing to Architect's details	52	52	LM	4,500	4,500	234,000.00	234,000.00
	Total carried to Summary						1,508,160.00	1,987,055.00
	<u>FIRST FLOOR FINISHES</u>							
	<u>Walls Finishes</u>							
A.	15 mm thick cement : sand (1:4) plaster to external surfaces	93	109	SM	310	360	28,830.00	39,240.00
B	Lime plaster to internal masonry or concrete surfaces	280	280	SM	310	400	86,800.00	112,000.00
C	15 mm plaster backing to receive wall tiles	69	0	SM	290	360	20,010.00	-
	<u>External Painting</u>							
	<u>Three coats "Duracoat" pure acrylic outdoor protector</u>							
D	External wall and concrete surfaces	93	109	SM	400	400	37,200.00	43,600.00
	<u>Key Pointing</u>							

ITEM	DESCRIPTION	Bq Qty	Done	Unit	Bq Rate	Revised Rate	Bq Amount	Valuation
E	10 mm half round neat horizontal joints in external walls	145	36	SM	180	300	26,100.00	10,800.00
	<u>Ceramic wall tiles</u>							
F	8 mm thick coloured ceramic wall tiles as "Saj Ceramics"	69	0	SM	1,500	1,800	103,500.00	-
	<u>Internal Painting</u>							
	<u>Three coats first quality silk vinyl matt paint to :-</u>							
G	Internal masonry or concrete surfaces	280	280	SM	260	300	72,800.00	84,000.00
	<u>Floors</u>							
	<u>Cement : sand (1:4) in :-</u>							
A	42 mm thick paving ready to receive ceramic tiles	201	151	SM	400	450	80,400.00	67,950.00
	<u>Ceramic floor tiles</u>							
B	10 mm thick Ceramic floor tiles as "Saj Ceramics"	201	151	SM	1,600	2,200	321,600.00	332,200.00
	<u>Skirtings</u>							
C	100 mm ceramic tile skirting	94	87	LM	240	240	22,560.00	20,880.00
	<u>Granito floor tiles</u>							
*	10 mm thick Granito floor tiles		34	SM	3,500	3,500	-	119,000.00
	<u>Ceiling finishes</u>							
D	Acoustic Ceiling	285	0	SM	1,950	2,200	555,750.00	-
	<u>Gypsum ceiling</u>							
*	9 mm gypsum ceiling including lightweight steel suspension		266	SM	2,200	2,200	-	585,200.00
*	75 mm gypsum cornice		158	LM	450	450	-	71,100.00
	<u>Three coats first quality plastic emulsion matt paint to :-</u>							
*	Gypsum ceiling		266	SM	300	300	-	79,800.00
	<u>Balustrading and railing</u>							
F	900 mm high mild steel staircase railing to Architect's details	30	43	LM	4,500	4,500	135,000.00	193,500.00
	Total carried to Summary						1,490,550.00	1,759,270.00
	<u>ELEMENT NO. 5</u>							
	<u>WINDOWS – GROUND FLOOR</u>							
	<u>Window Cill</u>							
A	250 x 75 mm thick prec-cast concrete window cill	21	21	LM	750	750	15,750.00	15,750.00
	<u>Steel casement windows</u>							
B.	Window size 1800 x 1500 mm high	6		NO	21,750	17,300	130,500.00	-
C.	Window size 2400 x 1500 mm high	2		NO	28,500	28,800	57,000.00	-
D	Window size 600 x 600 mm high	3		NO	3,000	5,100	9,000.00	-
B.	Window size 1800 x 1600 mm high		5	NO	17,300	17,300	-	86,500.00
C.	Window size 2400 x 2000 mm high		3	NO	28,800	28,800	-	86,400.00
D	Window size 1400 x 600 mm high		3	NO	5,100	5,100	-	15,300.00
	Window size 1400 x 1600 mm high		1	NO	13,500	13,500	-	13,500.00
	Window size 1200 x 1600 mm high		1	NO	4,350	4,350	-	4,350.00
	<u>Glazing :-</u>							
	<u>4 mm thick clear sheet glass fixed to metal with putty:-</u>							
E	Panes 0.1 - 0.5 square metres	24	33	SM	1,600	1,600	38,400.00	52,800.00
F	Ditto but obscure glass ditto	1	3	SM	1,600	1,600	1,600.00	4,800.00
	<u>Apply three coats of gloss oil paint</u>							

ITEM	DESCRIPTION	Bq Qty	Done	Unit	Bq Rate	Revised Rate	Bq Amount	Valuation
A	Metal surfaces internally	25	36	SM	290	300	7,250.00	10,800.00
B	Metal surfaces externally	25	36	SM	290	300	7,250.00	10,800.00
	<u>Wrot Mahogany :-</u>							
C	150 x 125 mm pelmet box	21		LM	2,500	2,500	52,500.00	-
D	150 x 25 mm window board	17		LM	1,080	1,080	18,360.00	-
E	25 x 25 mm quadrant beading	17		LM	90	160	1,530.00	-
	<u>Three coats of clear polyurethane lacquer to :-</u>							
F	Wooden surfaces 200 - 300 mm	21		LM	90	120	1,890.00	-
G	Wooden surfaces 100 - 200 mm	17		LM	60	80	1,020.00	-
*	38 mm diameter brass curtain rods		22	LM	1,500	1,500	-	33,000.00
	Total carried to Summary						342,050.00	334,000.00
	<u>ELEMENT NO. 5</u>							
	<u>WINDOWS – FIRST FLOOR</u>							
	<u>Window Cill</u>							
A	250 x 75 mm thick prec-cast concrete window cill	21	21	LM	750	750	15,750.00	15,750.00
	<u>Steel casement windows</u>							
	Window size 1800 x 1500 mm high	6		NO	21,750	25,950	130,500.00	-
	Window size 2400 x 1500 mm high	2		NO	28,500	19,450	57,000.00	-
	Window size 600 x 600 mm high	3		NO	3,000	17,300	9,000.00	-
B.	Window size 2400 x 1800 mm high		4	NO	25,950	25,950	-	103,800.00
C.	Window size 1800 x 1800 mm high		2	NO	19,450	19,450	-	38,900.00
D	Window size 1600 x 1800 mm high		2	NO	17,300	17,300	-	34,600.00
*	Window size 1200 x 1600 mm high		1	NO	11,550	11,550	-	11,550.00
*	Window size 600 x 1600 mm high		1	NO	5,800	5,800	-	5,800.00
*	Window size 400 x 1100 mm high		1	NO	2,700	2,700	-	2,700.00
	<u>Glazing :-</u>							
	<u>4 mm thick clear sheet glass fixed to metal with putty:-</u>							
E	Panes 0.1 - 0.5 square metres	24	33	SM	1,600	1,600	38,400.00	52,800.00
F	Ditto but obscure glass ditto	1	0	SM	1,600	1,600	1,600.00	-
	<u>Apply three coats of gloss oil paint</u>							
A	Metal surfaces internally	25	33	SM	290	300	7,250.00	9,900.00
B	Metal surfaces externally	25	33	SM	290	300	7,250.00	9,900.00
	<u>Wrot Mahogany :-</u>							
C	150 x 125 mm pelmet box	21		LM	2,500	2,500	52,500.00	-
D	150 x 25 mm window board	17		LM	1,080	1,080	18,360.00	-
E	25 x 25 mm quadrant beading	17		LM	90	160	1,530.00	-
	<u>Three coats of clear polyurethane lacquer to :-</u>							
F	Wooden surfaces 200 - 300 mm	21		LM	90	120	1,890.00	-
G	Wooden surfaces 100 - 200 mm	17		LM	60	80	1,020.00	-
*	38 mm diameter brass curtain rods		26	LM	1,500	1,500	-	39,000.00
	Total carried to Summary						342,050.00	324,700.00
	<u>ELEMENT NO. 6</u>							
	<u>DOORS – GROUND FLOOR</u>							

ITEM	DESCRIPTION	Bq Qty	Done	Unit	Bq Rate	Revised Rate	Bq Amount	Valuation
	<u>Steel casement door</u>							
A	Double door overall size 1275 x 2400 mm high	1		NO	30,000	52,900	30,000.00	-
B	Double door overall size 1200 x 2400 mm high	1		NO	28,360	26,450	28,360.00	-
C	Double door overall size 1000 x 2400 mm high	1		NO	23,000	26,450	23,000.00	-
*	Double door overall size 1800 x 3000 mm high		1	NO		52,900	-	52,900.00
*	Double door overall size 900 x 3000 mm high		1	NO		26,450	-	26,450.00
*	Single door overall size 1200 x 2500 mm high		1	NO		29,400	-	29,400.00
*	Single door overall size 900 x 2200 mm high		1	NO		19,400	-	19,400.00
*	3 mm mild sheet cover to store at ramp area		2	SM		3,000	-	6,000.00
	<u>Timber Doors</u>							
	<u>45 mm solid cored flush door</u>							
D	Door size 900 x 2100 mm	2	5	NO	6,500	6,500	13,000.00	32,500.00
E	Door size 800 x 2100 mm	6	2	NO	5,500	6,500	33,000.00	13,000.00
E	Door size 1100 x 2300 mm		1	NO		8,700	-	8,700.00
	<u>Wrot Mahogany selected and kept clean :-</u>							
A	100 x 50 mm frame with labours	43	55	LM	960	1,440	41,280.00	79,200.00
B	50 x 25 mm architrave with two labours	43	48	LM	180	360	7,740.00	17,280.00
C	20 mm quarter-round beadings	43	48	LM	90	180	3,870.00	8,640.00
	<u>Supply and fix the following approved quality ironmongery</u>							
D	100 mm mild steel heavy duty butt hinges	12	16	PRS	180	250	2,160.00	4,000.00
E	Three lever aluminium mortice lock	2	1	NO	6,500	6,500	13,000.00	6,500.00
F	Two lever lock type English 'Union' lock	3	5	NO	2,300	3,500	6,900.00	17,500.00
G	Aluminium mortice bathroom lock 'Union' 680/66/94 lock	3	2	NO	1,500	3,500	4,500.00	7,000.00
H	Steel door lock	3	3	NO	7,500	7,500	22,500.00	22,500.00
I	Rubber door stop floor mounted	13		NO	240	250	3,120.00	-
J	Union coat and hat hook	3		NO	875	875	2,625.00	-
	<u>Aluminium wood primer to back of frame before fixing to :-</u>							
A	Surface 100 - 200 mm	43	43	LM	58	58	2,494.00	2,494.00
	<u>Three coats gloss oil paint to:-</u>							
B	General metal surfaces	16	29	SM	600	300	9,600.00	8,700.00
	<u>Three coats of clear polyurethane lacquer to :-</u>							
C	General timber surfaces	28	31	SM	320	400	8,960.00	12,400.00
D	Timber surface 100 - 200 mm girth	43	55	LM	64	80	2,752.00	4,400.00
	<u>Glazing</u>							
	<u>5 mm thick clear sheet glass fixed to timber</u>							
E	Panes 0.1 - 0.5 square metres	1	3	SM	3,600	3,600	3,600.00	10,800.00
	Total carried to Summary						262,461.00	389,764.00
	<u>ELEMENT NO. 6</u>							
	<u>DOORS – FIRST FLOOR</u>							
	<u>Steel casement door</u>							
A	Double door overall size 1200 x 2800 mm high	0	3	NO	32,915	32,915	-	98,745.00
B	Double door overall size 1275 x 2400 mm high	1	0	NO	30,000	28,360	30,000.00	-
B	Double door overall size 1200 x 2400 mm high	1	0	NO	28,360	28,360	28,360.00	-
	<u>Timber Doors</u>							
	<u>45 mm solid cored flush door</u>							
D	Door size 900 x 2300 mm	2	3	NO	6,500	7,100	13,000.00	21,300.00
E	Door size 800 x 2100 mm	6	0	NO	5,500	6,500	33,000.00	
*	Door size 1100 x 2300 mm	0	1	NO	8,700	8,700	-	8,700.00

ITEM	DESCRIPTION	Bq Qty	Done	Unit	Bq Rate	Revised Rate	Bq Amount	Valuation
	<u>Wrot Mahogany selected and kept clean :-</u>							
A	100 x 50 mm frame with labours	43	28	LM	960	1,440	41,280.00	40,320.00
B	50 x 25 mm architrave with two labours	43	24	LM	180	360	7,740.00	8,640.00
C	20 mm quarter-round beadings	43	24	LM	90	180	3,870.00	4,320.00
	<u>Supply and fix the following approved quality ironmongery</u>							
D	100 mm mild steel heavy duty butt hinges	12	8	PRS	180	250	2,160.00	2,000.00
E	Three lever aluminium mortice lock	2	1	NO	6,500	6,500	13,000.00	6,500.00
F	Two lever lock type English 'Union' lock	3	3	NO	2,300	3,500	6,900.00	10,500.00
G	Aluminium mortice bathroom lock 'Union' 680/66/94 lock	3	0	NO	1,500	3,500	4,500.00	
H	Steel door lock	2	3	NO	7,500	7,500	15,000.00	22,500.00
I	Rubber door stop floor mounted	13	0	NO	240	250	3,120.00	-
J	Union coat and hat hook	3	0	NO	875	875	2,625.00	-
	<u>Aluminium wood primer to back of frame before fixing to :-</u>							
A	Surface 100 - 200 mm	43	28	LM	58	58	2,494.00	1,624.00
	<u>Three coats gloss oil paint to:-</u>							
B	General metal surfaces	12	20	SM	600	300	7,200.00	6,000.00
	<u>Three coats of clear polyurethane lacquor to :-</u>							
C	General timber surfaces	28	18	SM	320	400	8,960.00	7,200.00
D	Timber surface 100 - 200 mm girth	43	28	LM	64	80	2,752.00	2,240.00
	<u>Glazing</u>							
	<u>5 mm thick clear sheet glass fixed to timber</u>							
E	Panes 0.1 - 0.5 square metres	1	2	SM	3,600	3,600	3,600.00	7,200.00
	Total carried to Summary						229,561.00	247,789.00
	Joinery Fittings							
*	Low level kitchen cabinet size 4300 x 600 x 900 mm high		1	NO		75,000	-	75,000.00
*	High level kitchen cabinet size 2450 x 600 x 300 mm high		1	NO		18,000	-	18,000.00
	Total carried to Summary						-	93,000.00
	<u>SUMMARY</u>							
	Substructures (provisional) :-						1,792,170.00	2,088,110.00
	Rc superstructure						2,170,645.00	2,170,645.00
	Walling						1,523,740.00	1,550,540.00
	Roof						1,466,090.00	1,523,372.00
	Finishes – ground floor						1,508,160.00	1,987,055.00
	Finishes – first floor						1,490,550.00	1,759,270.00
	Windows – ground floor						342,050.00	334,000.00
	Windows – first floor						342,050.00	324,700.00
	Doors – ground floor						262,461.00	389,764.00
	Doors – first floor						229,561.00	247,789.00
	Joinery Fittings						-	93,000.00
	TOTAL CARRIED TO SUMMARY						11,127,477.00	12,468,245.00

**Detailed Electrical Sub Contract Draft Final Account
Re-Measurements Bills of Quantities/**

ELECTRICAL INSTALLATIONS

The Contractor shall supply labour and supply, deliver, install, fix, connect, test, label and commission the works, clean, complete and working to every detail as described in the specification and by related specifications and on the drawings listed in the Schedule or Drawings to the satisfaction of the Consulting Engineers.

All lighting points shall as a mandatory requirement have cables from the conduit round box neatly concealed using a ceiling rose c/w a biscuit ring and upto 2 meters long 1.5mm sq 3 core white flex from the connector block to the Light fittings. 5Amp cable connector blocks must be used to connect the flex cable to the concealed cables. Pricing for this must be included in the rates.

A1 Lighting points and wiring

NB: All fittings to be as Deta or equal and approved unless otherwise advised by the Engineer

						As Installed		
ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)	QTY	RATE (Kshs.)	COST (Kshs.)
A1.01	1 way switching lighting points wired in 3x1.5mm ² PVC s/c copper cables drawn in 20mm dia. HG PVC conduits.	No.	27	1,100.00	29,700.00	78	975.00	76,050.00

A1.02	2 way switching lighting points wired in 3x1.5mm ² PVC s/c copper cables drawn in 20mm dia. HG PVC conduits. .	No.	47	1,100.00	51,700.00	15	1,050.00	15,750.00
A1.03	Intermediate switching lighting points wired in 3x1.5mm ² PVC s/c copper cables drawn in 20mm dia. HG PVC conduits. .	No.	2	1,200.00	2,400.00	4	1,200.00	4,800.00
A1.04	Total for Internal Lighting points & Wiring c/f to Electrical collection Page				83,800.00			96,600.00

A2 Light fittings

NB: All accessories to be strickly as MK, crabtree or equal and also all bulbs to be STRICTLY 8 Watts energy saving as Oslam, Philips or equal and approved unless otherwise adviced by the Engineer.

ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)	QTY	RATE (Kshs.)	COST (Kshs.)
A2.01	6A 1 gang 1way plate switch	No.	10	250.00	2,500.00	-	-	-
A2.02	6A 2 gang 1way plate switch	No.	1	250.00	250.00	-	-	-
A2.03	6A 1 gang 2 way plate switch	No.	6	250.00	1,500.00	9	200.00	1,800.00
A2.04	6A 2 gang 2 way plate switch	No.	2	250.00	500.00	11	250.00	2,750.00
A2.05	6A 3 gang 2 way plate switch	No.	1	350.00	350.00	2	300.00	600.00

A2.06	Intermediate switch plate	No.	1	450.00	450.00	1	400.00	400.00
A2.07	6A 1 gang 1way White Bakelite Architrave Switch as MK	No.	4	500.00	2,000.00	-	-	-
A2.08	600 x 600mm / 4x18W HPF recessed light fittings with Alluminium mirror louvre c/w Electronic Ballast to approval.	No.	14	4,500.00	63,000.00	-	-	-
A2.09	1200mm / 1x36W HF surface mounted bare flourescent batten with asymmetrical metal reflector cover and electronic ballast c/w tubes to approval.	No.	2	3,350.00	6,700.00	-	-	-

ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)	QTY	RATE (Kshs.)	COST (Kshs.)
A2.10	1200mm / 1x36W HF surface mounted bare fluorescent fitting with electronic ballast c/w tubes to approval.	No.	16	2,750.00	44,000.00	-	-	-
A2.11	1200mm / 1x36W surface mounted bare batten fluorescent waterproof fitting with electronic ballast c/w tubes to approval.	No.	2	3,000.00	6,000.00	-	-	-
A2.12	Round close ceiling fitting as 28W2D Thorn superclub	No.	10	2,500.00	25,000.00	-	-	-
A2.13	Close ceiling fitting as light flush luminaire with a polished brass chrome finish as micromark Futura MM18681 c/w energy saving bulbs for staircase, walkway and lobby areas	No.	18	2,850.00	51,300.00	-	-	-
A2.14	Decorative security perimeter fitting as Thorn concept two grills bulkhead c/w energy saving bulbs .	No.	6	2,850.00	17,100.00	-	-	-

A2.15	Waterproof mirror light to approval. IP65 rated.	No.	6	2,500.00	15,000.00	2	900.00	1,800.00
A2.16	Self contained single sided pendant white exit sign with 8W fluorescent tube non maintained emergency lighting for 3hours duration as Thorn status ESX3	No.	5	7,500.00	37,500.00	5	5,000.00	25,000.00
A2.17	Total for Lighting fittings c/f to Electrical collection Page				273,150.00			32,350.00

A3 Power outlets conduiting & wiring

ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)	QTY	RATE (Kshs.)	COST (Kshs.)
A3.01	Ring mains socket outlets in 3x 2.5mm ² PVC CU cables drawn in 20mm HG PVC conduits.	No.	19	1,450.00	27,550.00	20	1,150.00	23,000.00
A3.02	Ditto for hand drier outlet point	No.	6	1,450.00	8,700.00	2	1,150.00	2,300.00
A3.03	Ditto for fire alarm system outlet point	No.	1	1,450.00	1,450.00	1	1,150.00	1,150.00
A3.04	Cooker outlet point wired in 3 x 6.0mm ² PVC s/c CU cables in 25mm dia the concluded conduits	No.	1	3,000.00	3,000.00	1	3,000.00	3,000.00
A3.05	Undersink water heater power point wired in 3 x 2.5mm ² CU cables drawn In 20mm Ø HG PVC conduits via a DP Switch .	No.	1	1,750.00	1,750.00	1	1,750.00	1,750.00
A3.06	Fire alarm call outlet point complete with draw wire done in 25mm HG PVC conduits	No.	23	650.00	14,950.00	1	650.00	650.00

A3.07	Data and telephone outlet points complete with draw wire done in 25mm HG PVC conduits	No.	7	650.00	4,550.00	16	650.00	10,400.00
A3.08	TV outlet points complete with draw wire done in 25mm HG PVC conduits	No.	1	650.00	650.00	5	650.00	3,250.00
A3.09	3 x 32mm Ø HG PVC conduits for linking trunking in offices	Lm.	15	300.00	4,500.00	15	300.00	4,500.00
A3.10	Purpose made compartmentalised adaptable boxes for Power, TV and Intercom to Engineer's detail and to approval	No.	3	1,000.00	3,000.00	5	700.00	3,500.00
A3.11	Total for power conduiting and wiring c/f to Electrical collection Page				42,550.00			53,500.00

A4 Power outlets accessories

NB: All fittings to be as MK, crabtree or equal and approved unless otherwise advised by the Engineer.

ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)	QTY	RATE (Kshs.)	COST (Kshs.)
A4.01	13A twin switched socket plate c/w neon indicator	No.	19	550.00	10,450.00	20	450.00	9,000.00
A4.02	45 A DP switched cooker control units with neon indicator faceplate marked cooker as crabtree Ref No 4520/31	No.	1	1,500.00	1,500.00	1	2,000.00	2,000.00
A4.03	45A cable outlet as crabtree ref No. 4506	No.	1	600.00	600.00	1	300.00	300.00
A4.04	20A DP controled standard switch with neon indicator for water heater	No.	8	550.00	4,400.00	4	500.00	2,000.00

A4.05	20A cord outlet plate standard	No.	8	650.00	5,200.00	4	650.00	2,600.00
A4.06	TV co-axial dual socket plate.	No.	1	550.00	550.00	5	300.00	1,500.00
A4.07	Dual socket plate for Data RJ45 and Telephone RJ 11 as siemon	No.	7	850.00	5,950.00	-	-	-
A4.08	Total for power outlet fittings c/f to the to Electrical collection Page				18,200.00			17,400.00

A5 Power distribution, cabling & switchgears

NB: All fittings to be as Merlin Gerin, Crabtree, Havel originals and cables to be as kenwestfal or E.A cables or equal and approved unless otherwise advised by the Engineer.

ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)	QTY	RATE (Kshs.)	COST (Kshs.)
A5.01	6 way Power Distribution Board DBR'. Bus bars and Integral isolator rated at 100A TPN.	No.	1	12,500.00	12,500.00	1	8,200.00	8,200.00
A5.02	6 way Consumer's Unit CU'F'.& CU'CL'	No.	2	3,000.00	6,000.00	2	2,500.00	5,000.00
A5.03	10A SP MCB	No.	6	550.00	3,300.00	4	400.00	1,600.00
A5.04	20A SP MCB	No.	7	550.00	3,850.00	6	400.00	2,400.00

A5.05	30A SP MCB	No.	2	550.00	1,100.00	6	400.00	2,400.00
A5.06	40A SP MCB	No.	2	700.00	1,400.00	-	-	-
A5.07	SP Blanking plates	No.	8	100.00	800.00	-	-	-
A5.08	TP Blanking plates	No.	2	150.00	300.00	-	-	-
ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)	QTY	RATE (Kshs.)	COST (Kshs.)
A5.09	16mm ² 4C PVC SWA PVC CU cable C/W cable glands and cable lugs from meter board to the power distribution (Subject to site remeasurement)	LM	80	1,150.00	92,000.00	-	-	-
A5.10	50mm Ø HG PVC conduits sleeves for the above.	LM	15	200.00	3,000.00	15	482.00	7,230.00

A5.11	2 x 10.0 +10.0mm ² e.c.c. PVC S/C CU cables drawn 32mm Ø HG PVC conduits from the power distribution board in the ground floor to the consumer units in First floor.	LM	20	550.00	11,000.00	70	510.00	35,700.00
A5.12	63A TPN Isolator control switch for Systems with weatherproof enclosure as Hager.	No.	1	4,500.00	4,500.00	1	8,000.00	8,000.00
A5.13	100A TPN MCCB as Hager.	No.	1	2,500.00	2,500.00	1	8,000.00	8,000.00
A5.14	Protective multiple earthing	No.	1	1,500.00	1,500.00	1	1,500.00	1,500.00
A5.15	Labelling of DB's and CU's and final sub-circuits.	Item	1	1,000.00	1,000.00	1	1,000.00	1,000.00

A5.16	Total for Power distribution, cabling and switchgears c/f to Electrical collection Page				144,750.00			81,030.00
-------	---	--	--	--	------------	--	--	-----------

ELECTRICAL PRICE COLLECTION PAGE

ITEM	DESCRIPTION	COST (Kshs.)	
1	Lighting points and wiring	83,800.00	96,600.00
2	Light fittings	273,150.00	32,350.00
3	Power outlets conduiting & wiring	42,550.00	53,500.00
4	Power outlets accessories	18,200.00	17,400.00
5	Power distribution, cabling & switchgears	144,750.00	81,030.00
6	Allow Sum for generation of As built drawings, testing & Commissioning of all the installations.	15,000.00	-

7	Contingency	70,000.00	-
8	Total Without VAT	647,450.00	280,880.00
9	Add: 16% VAT	103,592.00	44,940.80
10	Total for Electrical installation Inclusive V.A.T c/f to BUILDERS WORK form of tender	751,042.00	325,820.80

ELECTRICAL INSTALLATIONS**A1 Trunking installations and Power point**

The Contractor shall supply labour and supply, deliver, install, fix, connect, test, label and commission the works, clean, complete and working to every detail as described in the specification and by related specifications and on the drawings to the satisfaction of the Consulting Engineers.

						<i>As Installed</i>		
ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)	QTY	RATE (Kshs.)	COST (Kshs.)
A1.01	250 x 50mm, 3 compartments stove enamelled factory fabricated metallic trunking complete with angle bends, Tees and end caps to detail and to approval. Includes equipotential bonding c/w fixing accessories such as rawl bolts, brackets, clamps, fasteners etc. Colour to be approved and bonded to earth after every 10M	LM	55	1,850.00	101,750.00	100	847.20	84,720.00
A1.02	Trunking faceplates for twin socket outlets	No.	14	450.00	6,300.00	25	450.00	11,250.00

A1.03	Trunking faceplates for RJ45 single socket outlets.	No.	14	450.00	6,300.00	-	-	-
A1.04	Trunking faceplates for twin Clean power outlets.	No.	14	450.00	6,300.00	-	-	-
A1.05	Trunking faceplates for A/C unit outlets	No.	1	450.00	450.00	-	-	-
A1.06	Trunking faceplates for UPS outlets	No.	1	450.00	450.00	-	-	-

ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)	RATE (Kshs.)		
A1.07	RAW POWER; Ring mains socket outlets in 2.5mm ² PVC - Insulated twin + earth CU cables.	No.	6	1,750.00	10,500.00	25	1,150.00	28,750.00
A1.08	RAW POWER; 13A twin switched socket plate for the above as MK	No.	6	950	5,700.00	25	450	11,250.00
A1.09	CLEAN POWER; Clean power outlets wired in 2.5mm ² twin +earth PVC-insulated CU cables	No.	5	1,750.00	8,750.00	15	1,150.00	17,250.00
A1.10	CLEAN POWER; 13A twin non switched socket plate for the above as MK	No.	5	1250	6,250.00	-		0

A1.11	CABINET; Industrial socket outlet point wired in 6.0mm ² twin +earth PVC-insulated CU cables	No.	1	7,500.00	7,500.00	-	-	-
A1.12	CABINET; 32A Industrial Sockets with male / female (Single phase) for Termination to the cabinets as MEM or MK.	No.	1	5,000.00	5,000.00	-	-	-
A1.13	CABINET; Wiring in 3 core 4.0mm ² Flex cable from the clean power board to the PDU's in the cabinets via a industrial socket. (BLACK CABLES)	No.	1	6,500.00	6,500.00	-	-	-
ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)	RATE (Kshs.)		
A1.14	UPS; 40A by-pass 4 pole switches for UPS connection inclusive of a minimum of 10mm ² 4 core cable for sub mains to feed UPS intake	No.	1	12,500.00	12,500.00	-	-	-

A1.15	AC ; Single phase AC unit outlet points wired in 2.5mm ² twin + earth PVC insulated CU cables.	No.	1	4000	4,000.00	0		-
A1.16	AC ; 20A SPN control switch for single phase AC unit	No.	1	2500	2,500.00	0		-
A1.17	AC ; 20A DP control switch for single phase A/C indoor and outdoor unit and its wiring .	No.	2	800.00	1,600.00	-		-
A1.18	Patress boxes for Twin sockets	No.	1	195	195.00	0		-

A1.19	Total for Trunking installations and Power Supply c/f to the Price Summary Page				192,545.00			153,220.00
-------	---	--	--	--	------------	--	--	------------

A2 Power Supply to workstations**NB:** All accessories to be as MK or unless otherwise advised by the Engineer

ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)	RATE (Kshs.)		
A2.01	RAW POWER; Ring mains socket outlets in 2.5mm ² PVC - Insulated twin + earth CU cables.	No.	6	1750	10,500.00			
A2.02	RAW POWER; 13A twin switched standard socket plate for the above as MK	No.	6	950	5,700.00			
A2.03	RAW POWER; DP control switch outlet point wired in 3 x 4.0mm cu cables.	No.	2	2500	5,000.00			
A2.04	RAW POWER; 20A fused, switched DP control switch with neon indicator	No.	2	800	1,600.00			
A2.05	CLEAN POWER; Clean power outlets wired in 2.5mm ² twin +earth PVC-insulated CU cables	No.	5	1300	6,500.00			
A2.06	CLEAN POWER; 13A twin, switched, shuttered socket plates with neon light for clean supply as MK non-standard, but with 10mm high red traffolyte labels namely "U.P.S Supply"	No.	5	2500	12,500.00			

A2.07	CLEAN POWER; DP control switch outlet point wired in 3 x 4.0mm cu cables.	No.	2	2500	5,000.00			
A2.08	CLEAN POWER; 20A fused, switched DP control switch with neon indicator	No.	2	800	1,600.00			
A2.09	3M power flylead cable with male / female ICE socket as RS in the computer power cables	No.	10	300	3,000.00			
A2.10	Top plug for the MK non-standard sockets. Cost to include labour for installing in the computer power cables	No.	10	500	5,000.00			
A2.11	Total for Power Supply to workstations c/f to price collection page				56,400			

A3 Fire detection and alarm system

Makes quoted to be as Menvier, Gent, Kidde, GE. Other makes are subject to Engineers consent and approval.

ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)	RATE (Kshs.)		
A3.01	Fire alarm break glass unit.	No.	6	4,500.00	27,000.00	5	400.00	2,000.00
A3.02	Wall mounted Loop powered wall sounder combined with a flasher beacon (as one unit)	No.	6	6,500.00	39,000.00	1	3,100.00	3,100.00
A3.03	Heat detector.	No.	1	3,500.00	3,500.00	1	2,200.00	2,200.00
A3.04	Smoke detector.	No.	10	3,500.00	35,000.00	11	2,400.00	26,400.00
A3.05	2 zone fire alarm panel, Must have a volt - free contact where the Security alarm panel will be interlinked.	No.	1	45,000.00	45,000.00	1	43,000.00	43,000.00
A3.06	Programing of the above	No.	1	10,000.00	10,000.00	1	10,000.00	10,000.00

A3.07	Wiring of fire alarm call points using 1.5mm ² fire resistant cable as FIRETEC or FP200.	No.	23	1,550.00	35,650.00	19	1,550.00	29,450.00
A3.08	Providing a volt-free contact / port for interconnecting to the security alarm panel	Item	1	4,000.00	4,000.00	1	4,000.00	4,000.00
A3.09	Total for Fire Alarm System installations c/f to price summary page.				199,150.00			120,150.00

ELECTRICAL PRICE SUMMARY PAGE

ITEM	DESCRIPTION	COST (Kshs.)	COST (Kshs.)
1	Trunking installations and Power point	192,545.00	153,220.00
2	Power Supply to workstations	56,400.00	-
3	Fire detection and alarm system	199,150.00	120,150.00
4	Allow sum for UPS Supply and installation	250,000.00	
5	Allow sum for MATV system	40,000.00	
6	Allow sum for Structured Cabling supply and install	694,108.00	
7	Allow Sum for generation of As built drawings, testing & Commissioning of all the installations.	15,000.00	

8	Contingency	100,000.00	
9	Total Without VAT	1,447,203.00	273,370.00
10	Add: 16% VAT	231,552.48	43,739.20
11	Total for Electrical installation Inclusive V.A.T c/f to BUILDERS WORK form of tender	1,678,755.48	317,109.20

ITEM	DESCRIPTION	UNIT	QTY	RATE (Kshs.)	COST (Kshs.)
1.00	Light Fittings				
a	600x600mm recessed 36W LED panels	No.	4	2,700.00	10,800.00
b	18W circular LED pencil Lights	No.	34	2,000.00	68,000.00
c	30W LED Bulhead Security Lights	No.	6	3,000.00	18,000.00
d	12W LED Recessed Downlighters	No.	43	1,800.00	77,400.00
2.00	Switches				
a	6A 2 gang 1way White Bakelite Architrave Switch as MK	No	3	500.00	1,500.00
b	4 Gang 2 way switch as MK	No	1	300.00	300.00
3.00	Cable				
a	25mm ² 4C PVC SWA PVC CU cable C/W cable glands and cable lugs from meter board to the power distribution (Subject to site remeasurement)	Lm	90	600	54,000
4.00	Power House				
a	Power House	Item	1	6000	6,000
b	Earth rod	Item	1	450	450
c	Single phase cut-outs	No.	3	750	2,250
5.00	Blanking Covers				
a	Circulars	No.	10	20	200
b	Square	No.	20	20	400
c	Twin	No.	15	30	450
6.00	Coaxial cable for TV	Rolls	2	3500	7,000
7.00	Tangilt 1/2 litre	Tins	3	600	1,800.00
8.00	Trunking wire	pcs	2	1440	2,880.00
	Total without VAT				251,430.00
	Add 16% VAT				40,228.80
	Total for Extras c/f to price collection page				291,659

SUMMARY

Total B/F from Phase 1	325,820.80
Total B/F from Phase 2	317,109.20
Total B/F from Extras	291,659.00
WORK DONE AT SITE	934,589.00
LESS 10% RETENTION	93,458.90
SUB TOTAL	841,130.10

Detailed Plumbing & Drainage Sub Contract
Draft Final Account
Re-Measurements Bills of Quantities/

MECHANICAL INSTALLATIONS - PHASE I**A1 SANITARYWARE & FITTINGS - Supply & Install**

*Supply, deliver and fix the following sanitary fittings including all materials and jointings to supply, waste and overflow pipe fittings:-Note all sanitary fittings are coloured to project architect specific colour. **NB: Individual rates to be VAT inclusive***

CONTRACT SUMS

Item	Description	Unit	Qty	Rate (Kshs)	Amount (Kshs)
A1.01	Water Closet suite: Water closet as Nova Vista suite or equivalent with horizontal outlet, c/w both inlet and overflow 6 litres water cistern with English cistern fittings (Subject to approval), chrome plated levers, seat and cover with stainless steel bottom fixed hinges angle valve and 100mm diameter WC connectors	No.	4	35,000.00	140,000.00
A1.02	Disabled suite: Water closet pan Close-coupled as Twyford-doc.m Value Pack with white grab rails cat no. PK8184WH horizontal outlet. Doc.M value cistern, fittings and standard lever, Doc.M seat ring, stainless steel hinge, Hand rinse with no overflow, no chainstay, Spray mixer, lever operated mixing valve -thermostatic TMV3. Doc.M support rail (5 required). Doc.M hinged support rail and toilet roll holder. Wall hangers(pair), Grid waste, pan fixings, cistern cover clips, P trap outlet connector Cat.No WF1240WH.	No.	1	200,000.00	200,000.00
A1.03	Toilet roll holder: Toilet roll holder as Nova	No.	5	2,750.00	13,750.00
A1.04	Wash hand basin: Wall mounted 450mm Wash hand basin as nova or equivalent with one taphole and chain stay hole with Tapis Delayed action tap, chrome beaded chain 1½ mm chrome plated waste fittings cat. No. WF 4330 CP, white plastic bottle trap 1¼” P trap cat no. WF 8482xx and brackets to fit and the angle valve.	No.	4	12,500.00	50,000.00
A1.05	Mirror: 450x600mm silver plated plain glass mirror with bevelled edges and fixed with chrome plated screws and dome shaped cover.	No.	5	1,500.00	7,500.00

A1.06	Coat Hooks as Yideli or equivalent	No.	5	1,000.00	5,000.00
A1.07	Soap dispenser: Press type Liquid soap dispenser made out of enamel coat mild steel as Mediclinic or Equal and approved	No.	5	15,000.00	75,000.00
A1.08	Paper towel dispensers: Decorative wall mounted paper towel dispensers 230mm high, 300 mm wide and 100mm deep with easy tear holder and a spring loaded mechanism to release one sheet per pull. Removable lid and opens sides for towel level viewing and easy refilling complete with all accessories including a foot operated stainless steel disposed towel bin with cover (300mm high and 300mm diameter) All as Brickhouse, as Mediclinic or equal and approved.	No.	5	7,500.00	37,500.00
A1.09	Urinal bowl : 2 No. wall mounted Urinal bowls as Nova with exposed inlet, without flushing rim, for 1/2" connection, included jet nozzle, inlet-set, waste and bottle trap Ø 32mm model without cover (white in colour) with all fixing accessories included, complete with 1No high level 9 litres automatic cistern with inlet, 1no divider exposed flashpipes with bends and tees and any other necessary accessories.	Set	2	55,000.00	110,000.00
A1.10	Kitchen Sink: Single Bowl Single drainer Stainless Steel kitchen sink c/w chrome plated 1½" chrome plated bottle trap, 40mm chrome plated chain waste fitting(unslopped) cat. No WF 4343 CP and wall mounted swivel type kitchen sink mixer as Cobra Watertech Star 166-041 and all the other accessories.	No.	1	16,500.00	16,500.00
	Additional Sanitary Fittings				
A1.11	Hand dryers - Cost of supply only	No.	0		-
A1.12	Hand dryers - Cost of installation only	No.	0		-
A1.13	WC flush valves- Supply & Installation	No.	0		-
A1.14	Urinal Bowls - Supply & Installation	No.	0		-

A1.15	Urinal Flush Valve - Supply & Installation	No.	0		-
A1.16	5000 Liters pvc water tank with accessories - Supply & Installation	No.	0		-
A1.17	Terazzo cleaner's Sinks and accessories - Supply & Installation	No.	0		-
A1.18	Bib taps for cleaner's sink - Supply & Installation	No.	0		-
	Total for Sanitaryware & fittings c/f to price collection page				655,250.00

A2 Plumbing Works

Supply, deliver and fix the following in PPR-C (Polypropylene Random Copolymer) internal water pipework systems with fittings fixed and welding to be in accordance to the manufacturer's printed instructions as described. All PPR-C bends, Tees, reducing Tees, reducers etc. are to be formed in accordance to the manufacturer's printed instructions. The installations to have the various sizes of connectors, adaptors, sockets, reducers holdbats, clips etc. as required for satisfactory functions.

NOTE: The pipe diameters given are internal dimensions.

Item	Description	Unit	Qty	Rate (Kshs)	Amount (Kshs)
A2.01	15mm bore water pipes	Lm	20	125.00	2,500.00
A2.02	20mm bore water pipes	Lm	30	150.00	4,500.00
A2.03	25mm bore water pipes	Lm	60	220.00	13,200.00
	50mm bore water pipes	Lm	0	-	-
A2.04	25mm Bends and Elbows	No	30	160.00	4,800.00
A2.05	20mm Bends and Elbows	No	24	100.00	2,400.00
	50mm Bends and Elbows	No	0	-	-

A2.06	15mm Bends and Elbows	No	30	80.00	2,400.00
A2.07	25x20mm Reducer	No	20	150.00	3,000.00
A2.08	25x15mm Reducer	No	20	130.00	2,600.00
A2.09	20x15mm Reducer	No	8	100.00	800.00
A2.10	25mm Gate valves as peglar	No	10	2,150.00	21,500.00
A2.11	20mm Gate valves as peglar	No	6	1,800.00	10,800.00
	50mm Gate valves as peglar	No	0	-	-
A2.12	20x $\frac{1}{2}$ " Transition fittings	No	8	150.00	1,200.00
A2.13	25 x $\frac{3}{4}$ " Transition fittings	No	12	200.00	2,400.00
	50mm Sockets	No	0	-	-
A2.14	25mm Sockets	No	50	180.00	9,000.00
A2.15	20mm Ditto	No	16	150.00	2,400.00
A2.16	15mm Ditto	No	14	100.00	1,400.00

A2.17	15mm x 300mm long flexible connector complete with chrome plated stop cocks.	No	16	450.00	7,200.00
A2.18	20mm Float valve	No	2	500.00	1,000.00
A2.19	20mm screw thread nipple complete with 2No. Back nuts	No	2	200.00	400.00
A2.20	25mm screw thread nipple complete with 2No. Back nuts	No	2	280.00	560.00
A2.21	Water Storage Tanks: 1,500 Litres (330) PVC water storage tank dimensions 1310mm diameter x 1260mm high with a cover complete with all necessary backnuts,screw thread nipple etc for satisfactory functioning of the system. The tank to be asToptank or approved equivalent	No	2	23,500.00	47,000.00
A2.22	Water connection to the already existing Site water reticulation	item	1	15,000.00	15,000.00
A2.23	Testing and commissioning	item	1	5,000.00	5,000.00
A2.24	Total for Internal Plumbing works c/f to price collection page				161,060.00

A3 Internal Drainage

Supply, deliver and fix the following in UPVC soil and waste systems to BS 4514 and 5225 with fittings fixed in accordance to the manufacturer's printed instructions and BS 5572 and manufactured by "KEY TERRAIN" as described. All UPVC branches, Tees, reducing Tees, reducers etc. are to be formed in accordance to the manufacturer's printed instruction. The installations to have the various sizes of connectors, adaptors, sockets, reducers holdbats, clips etc. as required for satisfactory functions.

Item	Description	Unit	Qty	Rate (Kshs)	Amount (Kshs)
A3.01	100mm bore Heavy duty golden brown pipes	Lm	16	350.00	5,600.00

A3.02	100mm bore Heavy duty grey pipes	Lm	30	300.00	9,000.00
A3.03	50mm bore Heavy duty waste pipes	Lm	40	180.00	7,200.00
A3.04	40mm Ditto	Lm	10	120.00	1,200.00
A3.05	32mm Ditto	Lm	24	100.00	2,400.00
A3.06	100mm Sweep bend	No	13	440.00	5,720.00
A3.07	50mm Ditto	No	6	200.00	1,200.00
A3.08	40mm Ditto	No	8	150.00	1,200.00
A3.09	32mm Ditto	No	10	120.00	1,200.00
A3.10	50mm Tee	No	6	240.00	1,440.00
A3.11	40mm Ditto	No	4	200.00	800.00
A3.12	32mm Ditto	No	8	150.00	1,200.00
A3.13	50mm Inspection plug	No	2	180.00	360.00
A3.14	40mm Ditto	No	6	150.00	900.00

A3.15	32mm Ditto	No	8	120.00	960.00
A3.16	100mm diameter Vent cowl and Weathering slate to suite 100mm pvc pipe	No	2	1,200.00	2,400.00
A3.17	100 x 50 x 40 mm 4 way floor trap	No	8	1,500.00	12,000.00
A3.18	200mm diameter gulley trap c/w chamber and mild steel grating	No	2	3,500.00	7,000.00
A3.19	Testing and commissioning	item	1	5,000.00	5,000.00
A3.20	Total for internal drainage c/f to price Collection page				66,780.00

Price Collection Page - Sanitary fittings, plumbing & drainage Phase I

Item	Description	Costs (Kshs)
A1	Sanitaryware and Fittings - Supply & Install	655,250.00
A2	Plumbing works - Supply & Install	161,060.00
A3	Internal Drainage - Supply & Install	66,780.00
A4	Total for Mechanical installations <u>Inclusive of VAT</u> c/f Phase I Mechanical Price Summary Page	883,090.00

FINAL ACCOUNT BASED ON SITE RE-MEASUREMENTS

Qty Installed	Revised Rate with 10% mark-up (Kshs)	% Done	Amount (Kshs)	Omissions (Kshs)	Additions (Kshs)
0	38,500.00	0%	-	140,000.00	-
0	220,000.00	0%	-	200,000.00	-
3	3,025.00	100%	9,075.00	4,675.00	-
3	13,750.00	100%	41,250.00	8,750.00	-
2	1,650.00	100%	3,300.00	4,200.00	-

0	1,100.00	0%	-	5,000.00	-
3	16,500.00	100%	49,500.00	25,500.00	-
0	8,250.00	0%	-	37,500.00	-
0	60,500.00	0%	-	110,000.00	-
1	18,150.00	100%	18,150.00	-	1,650.00
			-		
3	12,000.00	100%	36,000.00	-	36,000.00
3	1,500.00	100%	4,500.00	-	4,500.00
3	15,000.00	100%	45,000.00	-	45,000.00
2	20,000.00	100%	40,000.00	-	40,000.00

2	15,000.00	100%	30,000.00	-	30,000.00
1	42,000.00	100%	42,000.00	-	42,000.00
2	4,200.00	100%	8,400.00	-	8,400.00
2	1,300.00	100%	2,600.00	-	2,600.00
			329,775.00	535,625.00	210,150.00

Qty Installed	Revised Rate with 10% mark-up (Kshs)	% Done	Amount (Kshs)	Omissions (Kshs)	Additions (Kshs)
0	137.50	0%	-	2,500.00	-
36	165.00	100%	5,940.00	-	1,440.00
42	242.00	100%	10,164.00	3,036.00	-
24	750.00	100%	18,000.00	-	18,000.00
35	176.00	100%	6,160.00	-	1,360.00
20	110.00	100%	2,200.00	200.00	-
6	400.00	100%	2,400.00	-	2,400.00

0	88.00	100%	-	2,400.00	-
20	165.00	100%	3,300.00	-	300.00
0	143.00	100%	-	2,600.00	-
0	110.00	100%	-	800.00	-
6	2,365.00	100%	14,190.00	7,310.00	-
1	1,980.00	100%	1,980.00	8,820.00	-
3	5,500.00	100%	16,500.00	-	16,500.00
10	165.00	100%	1,650.00	-	450.00
14	220.00	100%	3,080.00	-	680.00
5	350.00	100%	1,750.00	-	1,750.00
16	198.00	100%	3,168.00	5,832.00	-
10	165.00	100%	1,650.00	750.00	-
0	110.00	100%	-	1,400.00	-

4	495.00	100%	1,980.00	5,220.00	-
1	550.00	100%	550.00	450.00	-
1	220.00	100%	220.00	180.00	-
0	308.00	0%	-	560.00	-
0	25,850.00	0%	-	47,000.00	-
1	16,500.00	100%	16,500.00	-	1,500.00
1	5,500.00	100%	5,500.00	-	500.00
			116,882.00	89,058.00	44,880.00

Qty Installed	Revised Rate with 10% mark-up (Kshs)	% Done	Amount (Kshs)	Omissions (Kshs)	Additions (Kshs)
16	385.00	100%	6,160.00	-	560.00

54	330.00	100%	17,820.00	-	8,820.00
24	198.00	100%	4,752.00	2,448.00	-
12	132.00	100%	1,584.00	-	384.00
0	110.00	100%	-	2,400.00	-
13	484.00	100%	6,292.00	-	572.00
6	220.00	100%	1,320.00	-	120.00
8	165.00	100%	1,320.00	-	120.00
0	132.00	100%	-	1,200.00	-
6	264.00	100%	1,584.00	-	144.00
4	220.00	100%	880.00	-	80.00
8	165.00	100%	1,320.00	-	120.00
2	198.00	100%	396.00	-	36.00
6	165.00	100%	990.00	-	90.00

0	132.00	100%	-	960.00	-
1	1,320.00	100%	1,320.00	1,080.00	-
7	1,650.00	100%	11,550.00	450.00	-
4	3,850.00	100%	15,400.00	-	8,400.00
1	5,500.00	100%	5,500.00	-	500.00
			78,188.00	8,538.00	19,946.00

	Amount (Kshs)	Omissions (Kshs)	Additions (Kshs)
	329,775.00	535,625.00	210,150.00
	116,882.00	89,058.00	44,880.00
	78,188.00	8,538.00	19,946.00
	524,845.00	633,221.00	274,976.00

B PORTABLE FIRE EXTINGUISHERS - PHASE I

*Supply, deliver and install the following fire fighting equipment (stored in vandal proof protective cabinets) manufactured to BS EN3 and are in themselves something of established standard for quality around the world. **NB: Individual rates to be VAT inclusive***

CONTRACT SUMS

Item	Description	Unit	Qty	Rate (Kshs)	Amount (Kshs)
B1.01	5kg CO ₂ gas fire extinguisher	No	2	19,250.00	38,500.00
B1.02	9 Kg DCP fire extinguisher	No	2	21,500.00	43,000.00
B1.03	Fire blanket	No	1	8,000.00	8,000.00
B1.04	Total for portable Fire Extinguishers <u>Inclusive of VAT</u> c/f to Phase I Mechanical price summary page				89,500.00

FINAL ACCOUNT BASED ON SITE RE-MEASUREMENTS

Qty Installed	% Done	Amount (Kshs)	Omissions (Kshs)	Additions (Kshs)
0	0%	-	38,500.00	-
0	0%	-	43,000.00	-
0	0%	-	8,000.00	-
		-	89,500.00	-

MECHANICAL PRICE SUMMARY PAGE - PHASE I

ITEM	DESCRIPTION	CONTRACT TOTAL (KSHS.)	FINAL ACC TOTAL (KSHS.)	OMISSIONS (KSHS.)	ADDITIONS (KSHS.)
1	Sanitaryware & fittings, plumbing and Drainage- Supply and Install	883,090	524,845	633,221	274,976
2	Portable Fire Extinguishers - Supply and Install	89,500	-	89,500	-
3	<i>Contingency Sum</i>	<i>100,000</i>	-	100,000.00	-
4	Total For Phase I Mechanical Installations Inclusive of VAT c/f to Builders Work Phase I Price Summary Page	1,072,590	524,845	822,721	274,976

PLANCAD ASSOCIATES

PROJECT	PROPOSED TRAINING & RESOURCE CENTRE AT INSTITUTE OF PRIMATE RESEARCH - KAREN
EMPLOYER	NATIONAL MUSEUMS OF KENYA, INSTITUTE OF PRIMATE RESEARCH - KAREN
SERVICES ENGINEERS	PLANCAD ASSOCIATES
CONTRACTOR	EADSONS CONSTRUCTION AND ENGINEERING COMPANY
TITLE	PLUMBING & DRAINAGE FINAL ACCOUNT
DATE	4TH JUNE 2019

CONTRACT SUM	Kshs.	1,072,590.00
ADD: NET ADDITIONS	Kshs.	274,976.00
LESS: NET OMISSIONS INCLUDING CONTINGENCY SUM	Kshs.	822,721.00
FINAL ACCOUNT TOTAL INCLUSIVE OF 16% VAT	Kshs.	524,845.00

SIGNATURESTAMP & DATE.....

For: EADSONS CONSTRUCTION AND ENGINEERING COMPANY

SIGNATURESTAMP & DATE.....

For: PLANCAD ASSOCIATES - PROJECT SERVICES ENGINEERS

PLANCAD ASSOCIATES

ARCHSCAN ASSOCIATES LTD

P.O. BOX 10958 - 00100

NAIROBI


DATE: 4TH JUNE 2019

RE: VALUATION NO. 1 (PEN-ULTIMATE) FOR PLUMBING & DRAINAGE INSTALLATIONS

EMPLOYER	NATIONAL MUSEUMS OF KENYA, INSTITUTE OF PRIMATE RESEARCH - KAREN	
CONTRACTOR	EADSONS CONSTRUCTION AND ENGINEERING COMPANY	
PROJECT	PROPOSED TRAINING & RESOURCE CENTRE AT INSTITUTE OF PRIMATE RESEARCH - KAREN	
This valuation is issued by the Consultant pursuant to the terms of the Contract.		
CONTRACT SUM (VAT INCLUSIVE)		Kshs. 1,072,590.00
		Kshs.
a) GROSS FINAL WORK DONE (VAT INCLUSIVE)		524,845.00
b) LESS: RETENTION OF 5% OF GROSS VALUATION		26,242.25
c) LESS: AMOUNT PREVIOUSLY VALUAED		0.00
d) NET TOTAL AMOUNT DUE INCLUSIVE OF 16% VAT		498,602.75
SIGNEDSTAMP & DATE..... <i>For and on Behalf of Plancad Associates</i>		

CC: Eadsons Construction & Engineering Company

Installation /As Built Drawings
Architectural Layouts
Electrical layouts
Plumbing & Drainage Layouts

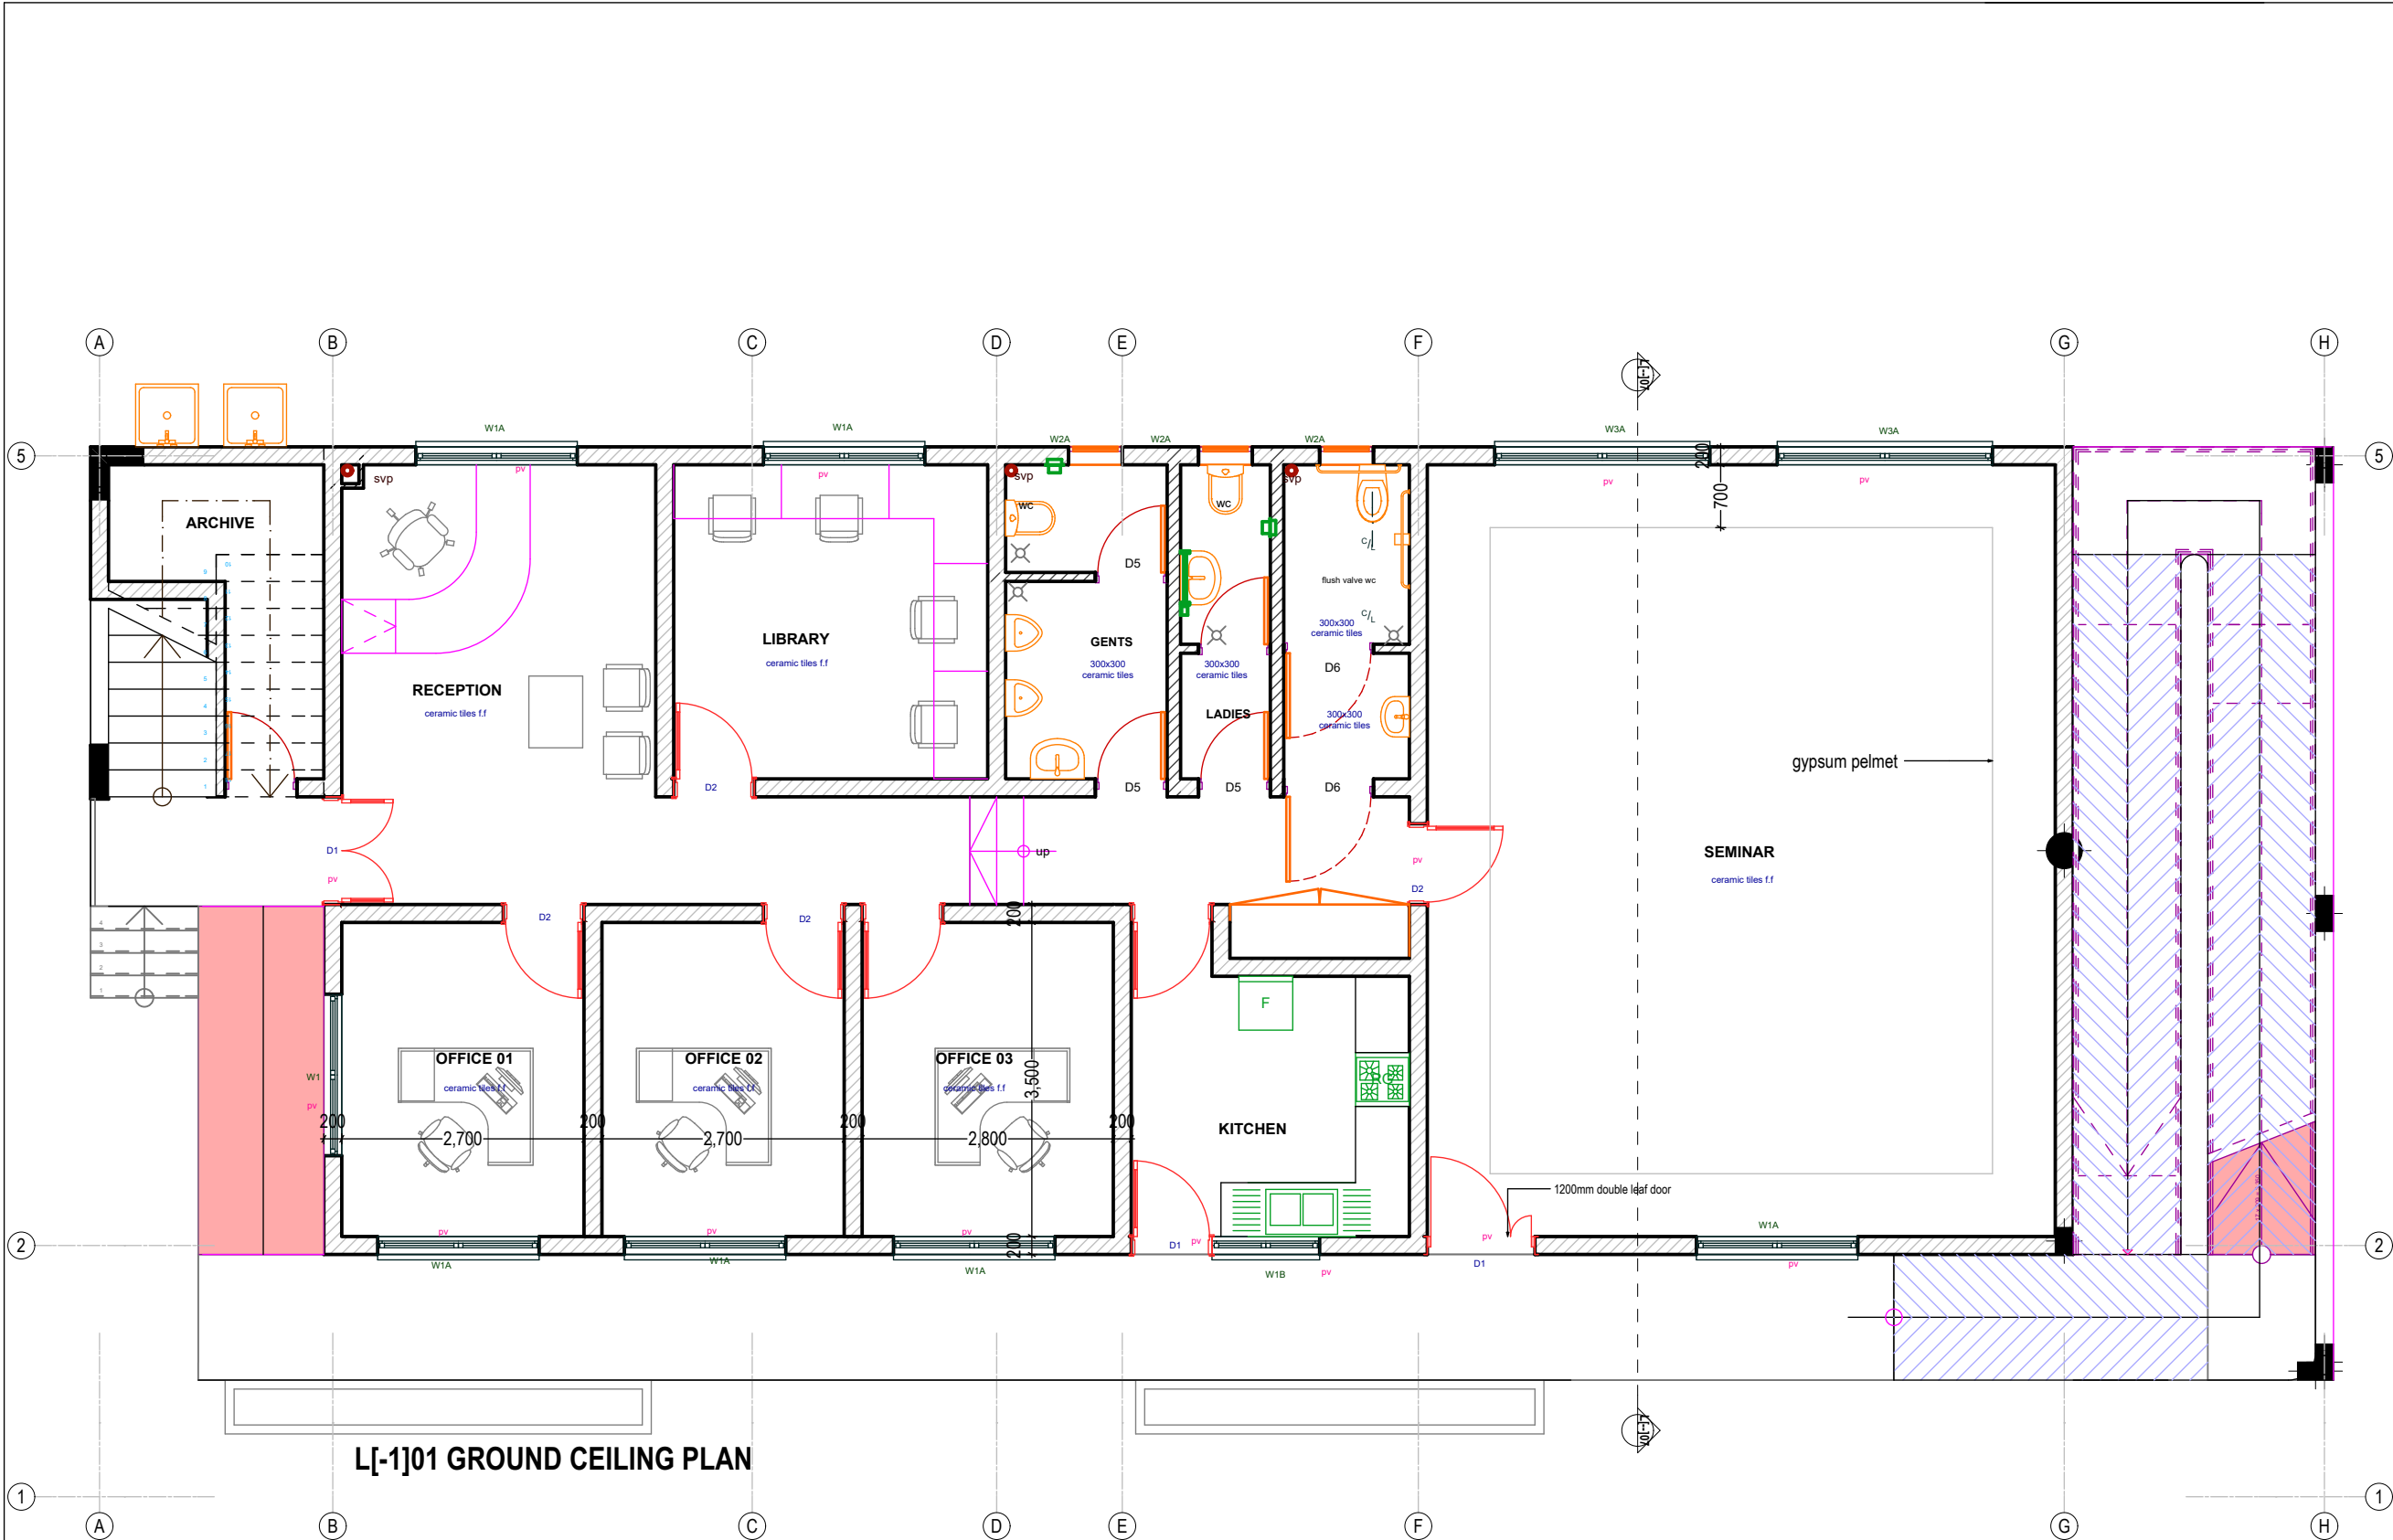

L[-1]01 GROUND CEILING PLAN

GENERAL NOTES

1. All dimensions are shown in mm unless otherwise specified
2. Drawings are not to be scaled. Only figured dimensions to be used
3. Contractor must check and verify all dimensions on site before commencing work
4. All slabs at ground level to be poured over 1000gauge polythene sheet DPM on
5. 50 mm thick some dust on approved grade hardcore filling
6. All soil under the slabs and all around external foundation to be treated with anti-termites insecticide

PUBLIC HEALTH (MOH)

1. All plumbing and drainage works to comply with NCC specifications
2. S.V.P. (soil vent pipes) to be provided at the head of the drainage
3. Drain passing underneath the buildings and drive ways to be encased in 150mm concrete surround
4. All underground drainage and waste pipes shall be uPVC to comply with BS 5255
5. All inspection chamber covers and framing cast iron in compliance with BS 497 Table 2 Grade A
6. Storm drain to comply with BS556
7. Minimum slope of drain pipes to be 1%
8. All testing of pipes must be complete before plastering
9. All mechanical works must be coordinated with electrical works. Any conflicts to be clarified before work begins
10. P.V. (permanent ventilations) and are to be provided above all openings EXCEPT doors to W/Cs
11. Provide standard septic tank to Structural Engineers specifications
12. Provide dustbin cubicle protected from animals and weather

FIRE NOTES

1. Provide 1x30m hose reel hydraulic tubing on each floor
2. Reserve 4500L water reservoir for firefighting only automatic booster pump to Mechanical Engineer's approval
3. Provide 2x9Kg CO2 Portable fire extinguishers in the passage and fire blankets for kitchens
4. Provide 2x9Kg CO2 fire extinguishers at each fire point
5. Install fire alarm emergency lighting system and smoke heat detectors
6. Provide fire exit signage and fire instruction notices

ELECTRICAL INSTALLATION

1. All electrical installation works are to comply with the specified requirements and should be carried out by a qualified electrician providing requisite test certificates upon completion and installation.
2. Works should be carried out in accordance to approved code of practise

WASTE MANAGEMENT SYSTEM

1. Septic tank constructed to Structural Engineers details
2. Provide Litter cubicles
3. Provide Litter bins

REV.	DATE	AMMENDMENT	BY:

project:
PROPOSED IPR TRAINING AND RESOURCE CENTRE


client:
NATIONAL MUSEUMS OF KENYA
P. O. Box 40658 - 00100,
NAIROBI.

architects:
ARCHSCAN ASSOCIATES LTD.
CONSULTING ARCHITECTS - INTERIOR DESIGNERS - PROJECT MANAGERS
Rose Avenue off Ngong Road
P. O. Box 10958 GPO-00100 Nairobi
Tel: +254 20 2738388/91, 20 2015662
Fax: +254 20 2728507, 20 2015662
Email: archscan@archscanassociates.com
website: www.archscanassociates.com

signature: _____

details:
CEILING DRAWING

drawn:	checked:	revision:	sign:
MAO	F.M.		
date:	scale:	project no.:	drawing no.
08.02.2019	NTS	MP/38	

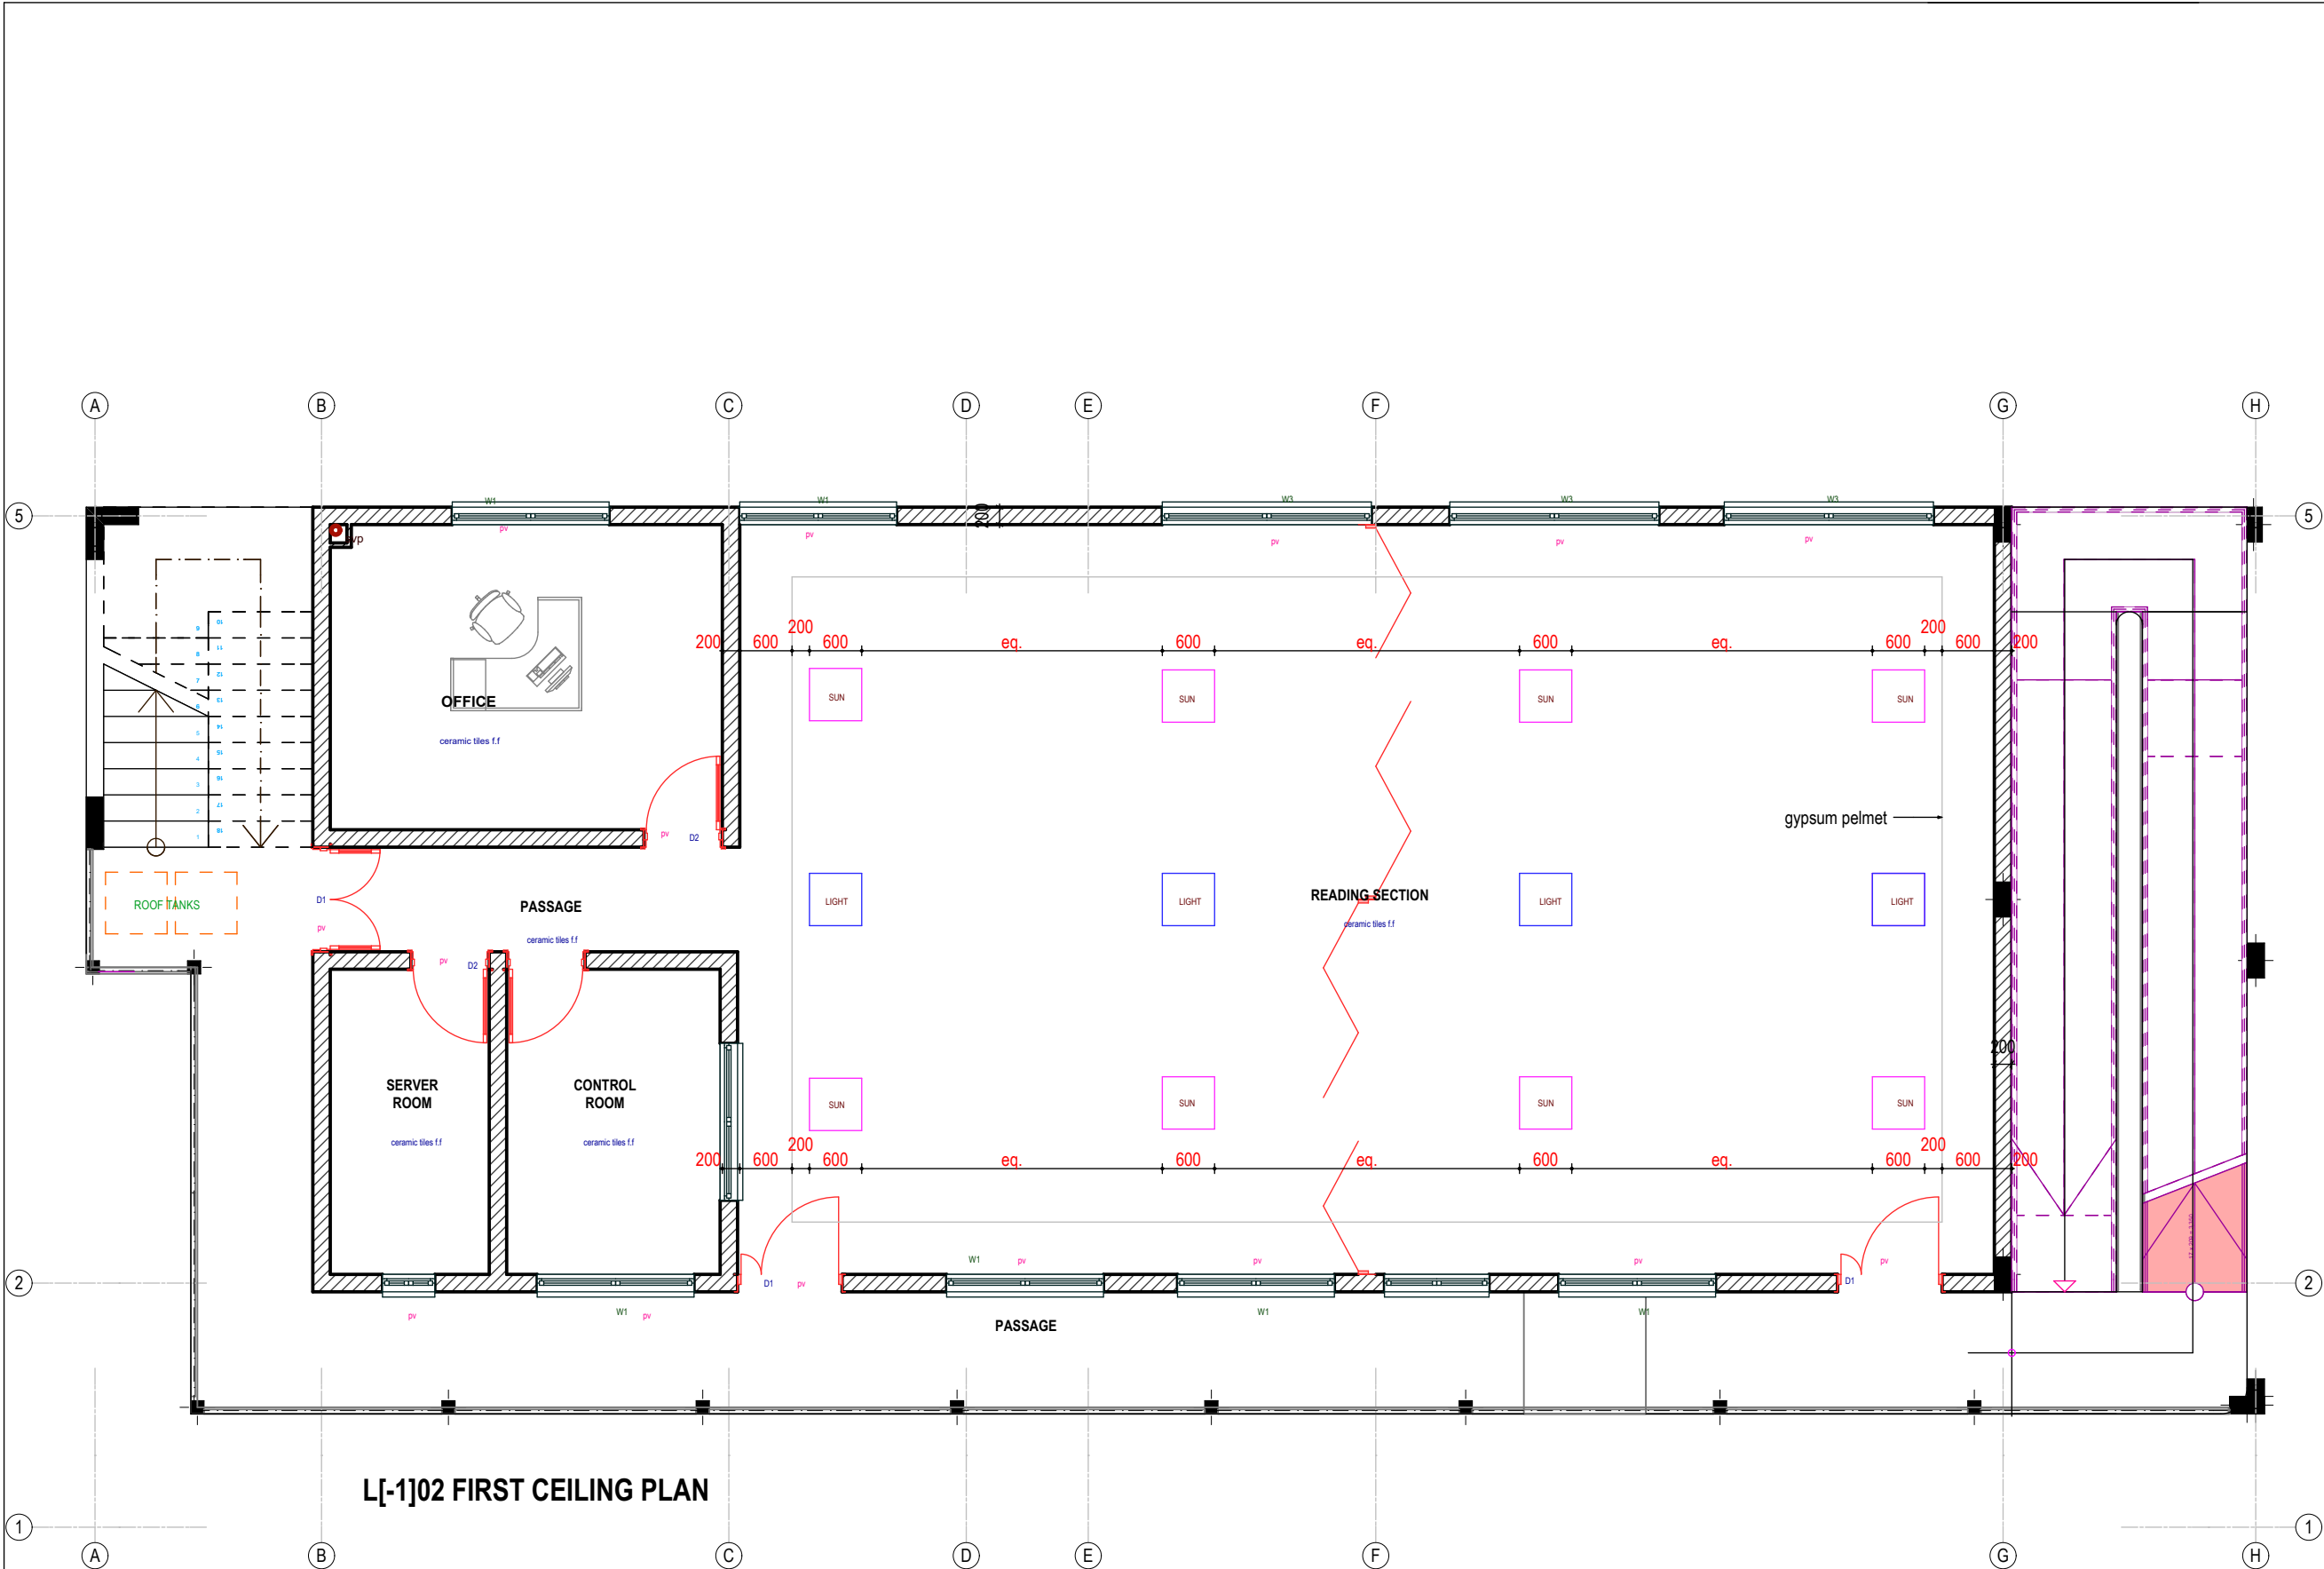

L[-1]02 FIRST CEILING PLAN

GENERAL NOTES

1. All dimensions are shown in mm unless otherwise specified
2. Drawings are not to be scaled. Only figured dimensions to be used
3. Contractor must check and verify all dimensions on site before commencing of work
4. All slabs at ground level to be poured over 1000gauge polythene sheet DPM on
5. 50 mm thick some dust on approved grade hardcore filling
6. All soil under the slabs and all around external foundation to be treated with anti-termites insecticide

PUBLIC HEALTH (MOH)

- 1.All plumbing and drainage works to comply with NCC specifications
- 2.S.V.P. (soil vent pipes) to be provided at the head of the drainage
- 3.Drain passing underneath the buildings and drive ways to be encased in 150mm concrete surround
- 4.All underground drainage and waste pipes shall be uPVC to comply with BS 5255
- 5.All inspection chamber covers and framing cast iron in compliance with BS 497 Table 2 Grade A
- 6.Storm drain to comply with BS556
- 7.Minimum slope of drain pipes to be 1%
- 8.All testing of pipes must be complete before plastering
- 9.All mechanical works must be coordinated with electrical works. Any conflicts to be clarified before work begins
- 10.PV (permanent ventilations) and are to be provided above all openings EXCEPT doors to W/Cs
- 11.Provide standard septic tank to Structural Engineers specifications
- 12.Provide dustbin cubicle protected from animals and weather

FIRE NOTES

- 1.Provide 1x30m hose reel hydraulic tubing on each floor
- 2.Reserve 4500L water reservoir for firefighting only automatic booster pump to Mechanical Engineer's approval
- 3.Provide 2x9Kg CO2 Portable fire extinguishers in the passage and fire blankets for kitchens
- 4.Provide 2x9Kg CO2 fire extinguishers at each fire point
- 5.Install fire alarm emergency lighting system and smoke heat detectors
- 6.Provide fire exit signage and fire instruction notices

ELECTRICAL INSTALLATION

- 1.All electrical installation works are to comply with the specified requirements and should be carried out by a qualified electrician providing requisite test certificates upon completion and installation.
- 2.Works should be carried out in accordance to approved code of practise

WASTE MANAGEMENT SYSTEM

1. Septic tank constructed to Structural Engineers details
- 2.Provide Litter cubicles
- 3.Provide Litter bins

REV.	DATE	AMMENDMENT	BY:

project:

PROPOSED IPR TRAINING AND RESOURCE CENTRE

client:

NATIONAL MUSEUMS OF KENYA
P. O. Box 40658 - 00100,
NAIROBI.

architects:

ARCHSCAN ASSOCIATES LTD.
CONSULTING ARCHITECTS INTERIOR DESIGNERS PROJECT MANAGERS
Rose Avenue off Ngong Road
P. O. Box 10958 GPO-00100 Nairobi
Tel: +254 20 2736398/91, 20 2015662
Fax: +254 20 2728507, 20 2015662
Email: archscan@archscanassociates.com
website: www.archscanassociates.com


signature: _____

details:

CEILING DRAWING

drawn:	checked:	revision:	sign:
MAO	F.M.		
date:	scale:	project no.:	drawing no.
08.02.2019	NTS	MP/38	

As Built – Electrical Drawings

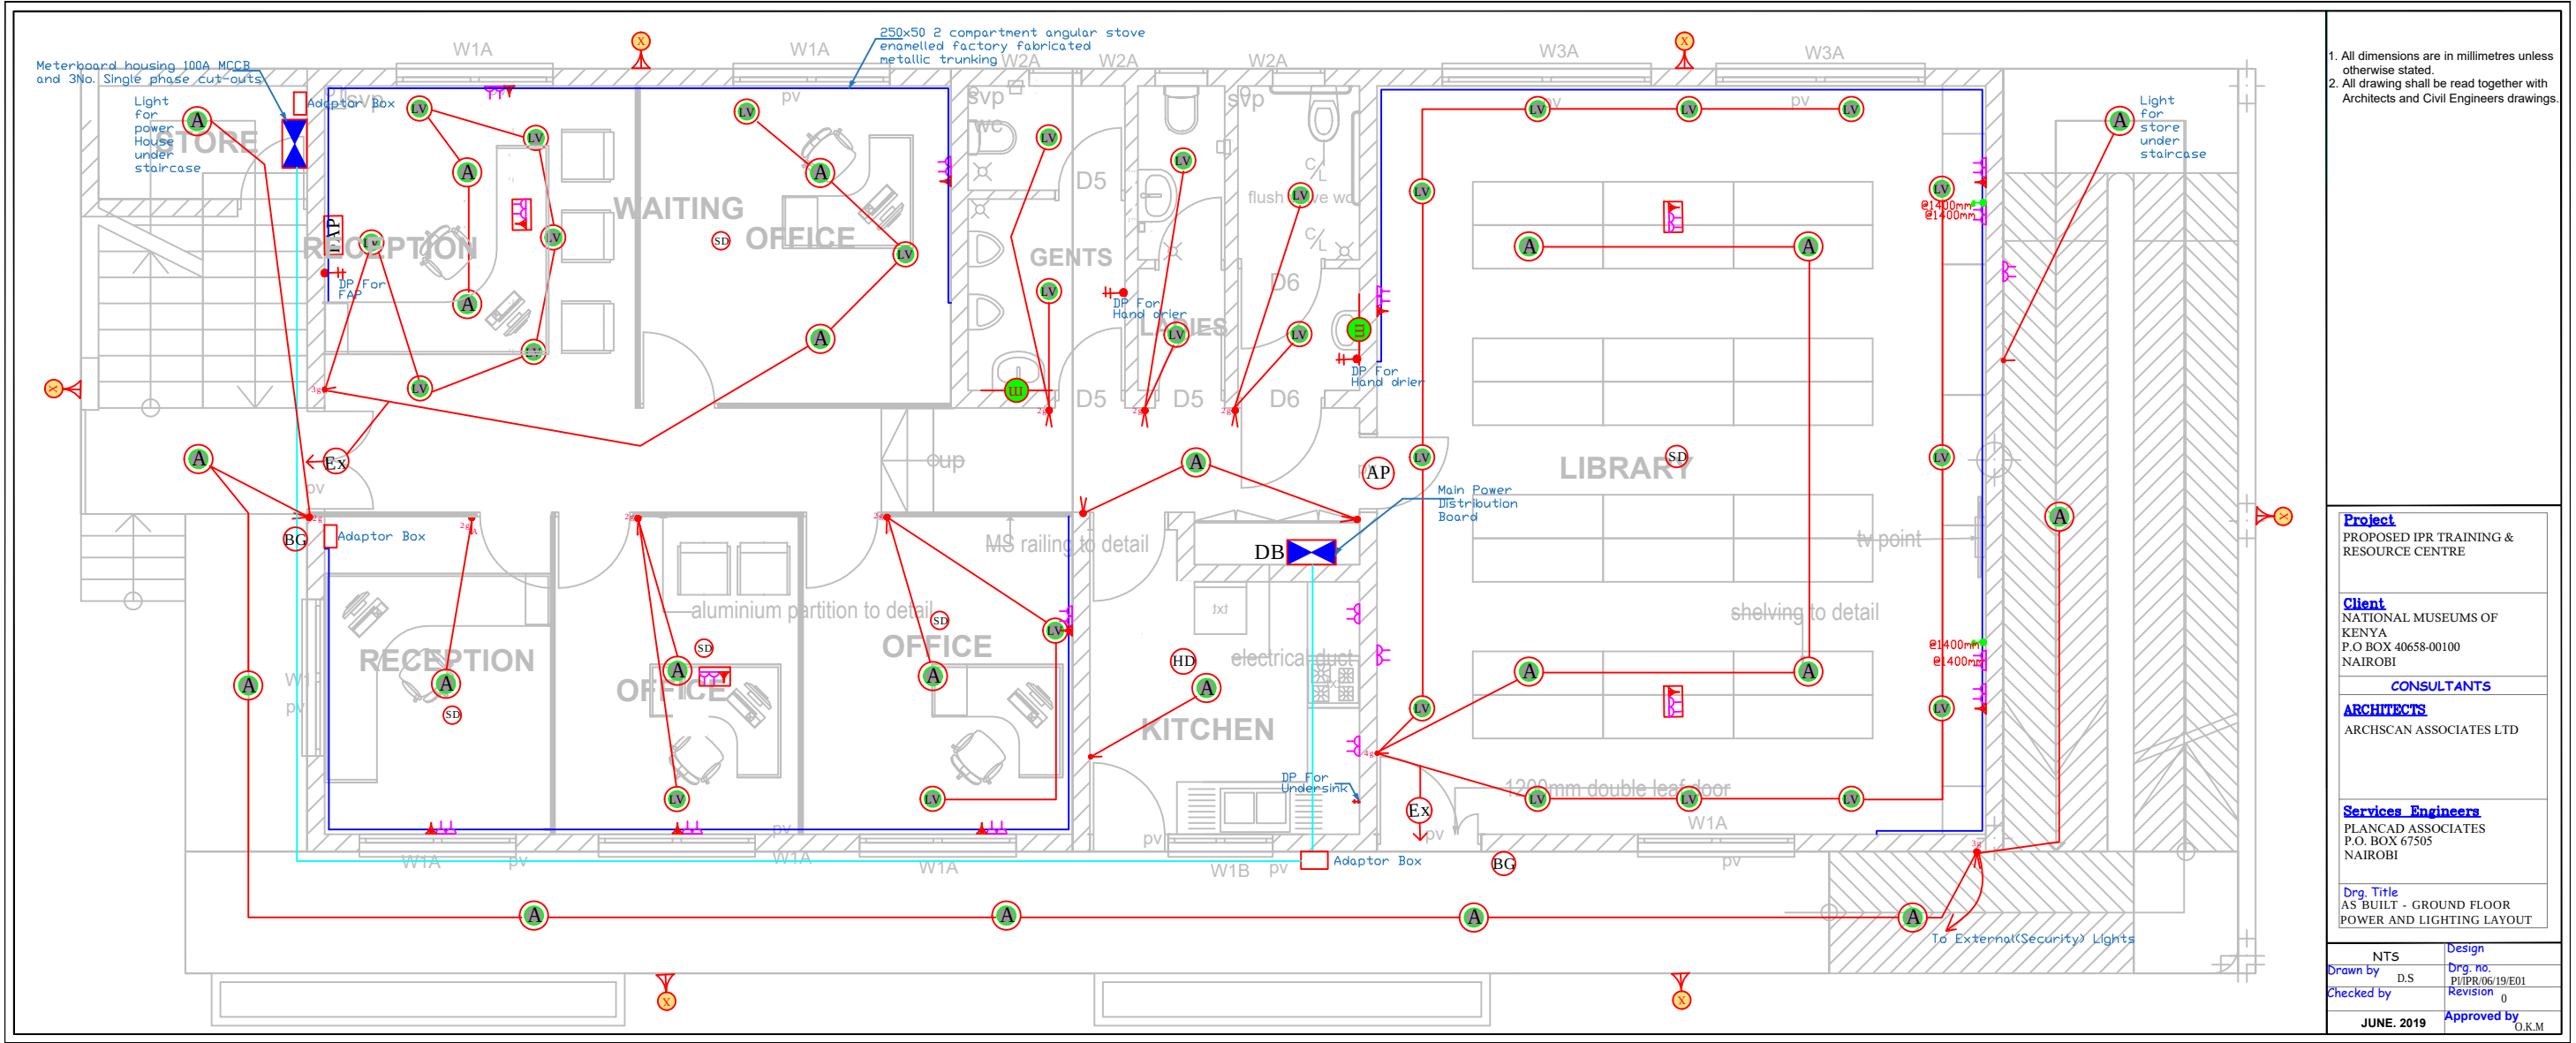

1. All dimensions are in millimetres unless otherwise stated.
2. All drawing shall be read together with Architects and Civil Engineers drawings.

Project PROPOSED IPR TRAINING & RESOURCE CENTRE	
Client NATIONAL MUSEUMS OF KENYA P.O BOX 40658-00100 NAIROBI	
CONSULTANTS ARCHITECTS ARCHSCAN ASSOCIATES LTD	
Services Engineers PLANCAD ASSOCIATES P.O. BOX 67505 NAIROBI	
Drg. Title AS BUILT - GROUND FLOOR POWER AND LIGHTING LAYOUT	
NTS	Design
Drawn by D.S	Drg. no. PI/PR/06/19/E01
Checked by	Revision 0
JUNE, 2019	Approved by O.K.M

POWER/LIGHTING LEGEND

SYMBOL	DESCRIPTION
	6A 1 gang 1 way SP plate switch
	6A 2 gang 1 way Architrave plate switch
	1/2/3/4 gang 2 way plate switch
	18W Circular LED Pencil Light
	12W Recessed LED Downlighters
	36W LED Bulkhead Security Light
	Water proof mirror light
	8W exit sign light
	600X600 Recessed 36W LED Panel Light

SYMBOL	DESCRIPTION
	13Amps Twin Switched Raw Power Socket Outlet
	Blanked Twin Switched Clean Power Socket Outlet
	13Amps Twin Switched Raw Power Socket Outlet
	20Amps Double Pole Switch
	Data/Voice Point
	TV Outlet Point
	Fire Alarm Smoke Detector
	Fire Alarm Heat Detector
	Wireless Access Point
	Break Glass
	Sounder
	Addressable Fire Alarm Panel
	Floor Box
	6 Way Main Power Distribution Board
	6 Way Raw Power Consumer Unit
	6 Way Clean Power Consumer Unit

1. All dimensions are in millimetres unless otherwise stated.
2. All drawing shall be read together with Architects and Civil Engineers drawings.

<u>Project</u> PROPOSED IPR TRAINING & RESOURCE CENTRE
<u>Client</u> NATIONAL MUSEUMS OF KENYA P.O BOX 40658-00100 NAIROBI
CONSULTANTS
<u>ARCHITECTS</u> ARCHSCAN ASSOCIATES LTD
<u>Services Engineers</u> PLANCAD ASSOCIATES P.O. BOX 67505 NAIROBI
<u>Drg. Title</u> AS BUILT - RECAP LIST

NTS	Design
Drawn by D.S	Drg. no. PI/IPR/06/19/E03
Checked by	Revision 0
JUNE. 2019	Approved by O.K.M

